
EXHIBIT 5

Activity ID	Activity Name	Original Duration	Start	Finish
Egida 387 -Guaynabo, P.R.		770	Feb-04-22	Jan-16-25
Project Start		105	Feb-04-22	Jul-05-22
CIC-4185	90% Construction Documents	10	Feb-04-22	Feb-17-22
CIC-4190	Submit for Permit	0		Feb-17-22
CIC-1505	Notice of Urbanization Permit in Hand	20	Feb-21-22	Mar-18-22
CIC-4135	Submit Tax Credit Application	5	Mar-21-22	Mar-25-22
CIC-4120	Notice of Tax Credit Award	20	Mar-28-22	Apr-22-22
CIC-4195	Investors Approval Process (Start to Finish)	20	Apr-26-22	May-23-22
CIC-1610	100% Construction Documents	10	May-24-22	Jun-06-22
CIC-4140	Final Construction Cost from GC	5	Jun-07-22	Jun-13-22
CIC-4160	Notice to Proceed	5	Jun-14-22	Jun-20-22
CIC-4145	Closing	13	Jun-14-22	Jun-30-22
CIC-4165	Mobilization & Insurances	10	Jun-20-22	Jul-01-22
CIC-4170	Procurement Start	0	Jun-21-22	
CIC-4150	Construction Permit	0		Jul-01-22
CIC-4155	Project Construction Start	0	Jul-05-22	
Procurement		317	Jun-21-22	Sep-06-23
Storm Sewer System		31	Jun-21-22	Aug-02-22
CIC-1020	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1025	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1030	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Sanitary Sewer System		31	Jun-21-22	Aug-02-22
CIC-1035	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1040	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1045	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Potable Water		31	Jun-21-22	Aug-02-22
CIC-1050	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1055	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1060	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Concrete Mix Design		20	Jun-21-22	Jul-18-22
CIC-1065	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1070	Submittal Approval	10	Jul-05-22	Jul-18-22
Reinforcement Steel		20	Jun-21-22	Jul-18-22
CIC-1080	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1085	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1090	Fabrication & Delivery	10	Jul-05-22	Jul-18-22
Forms		31	Jun-21-22	Aug-02-22
CIC-1095	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1100	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1105	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Roofing System		41	Jun-21-22	Aug-16-22
CIC-1170	Submittal Prep.	10	Jun-21-22	Jul-05-22

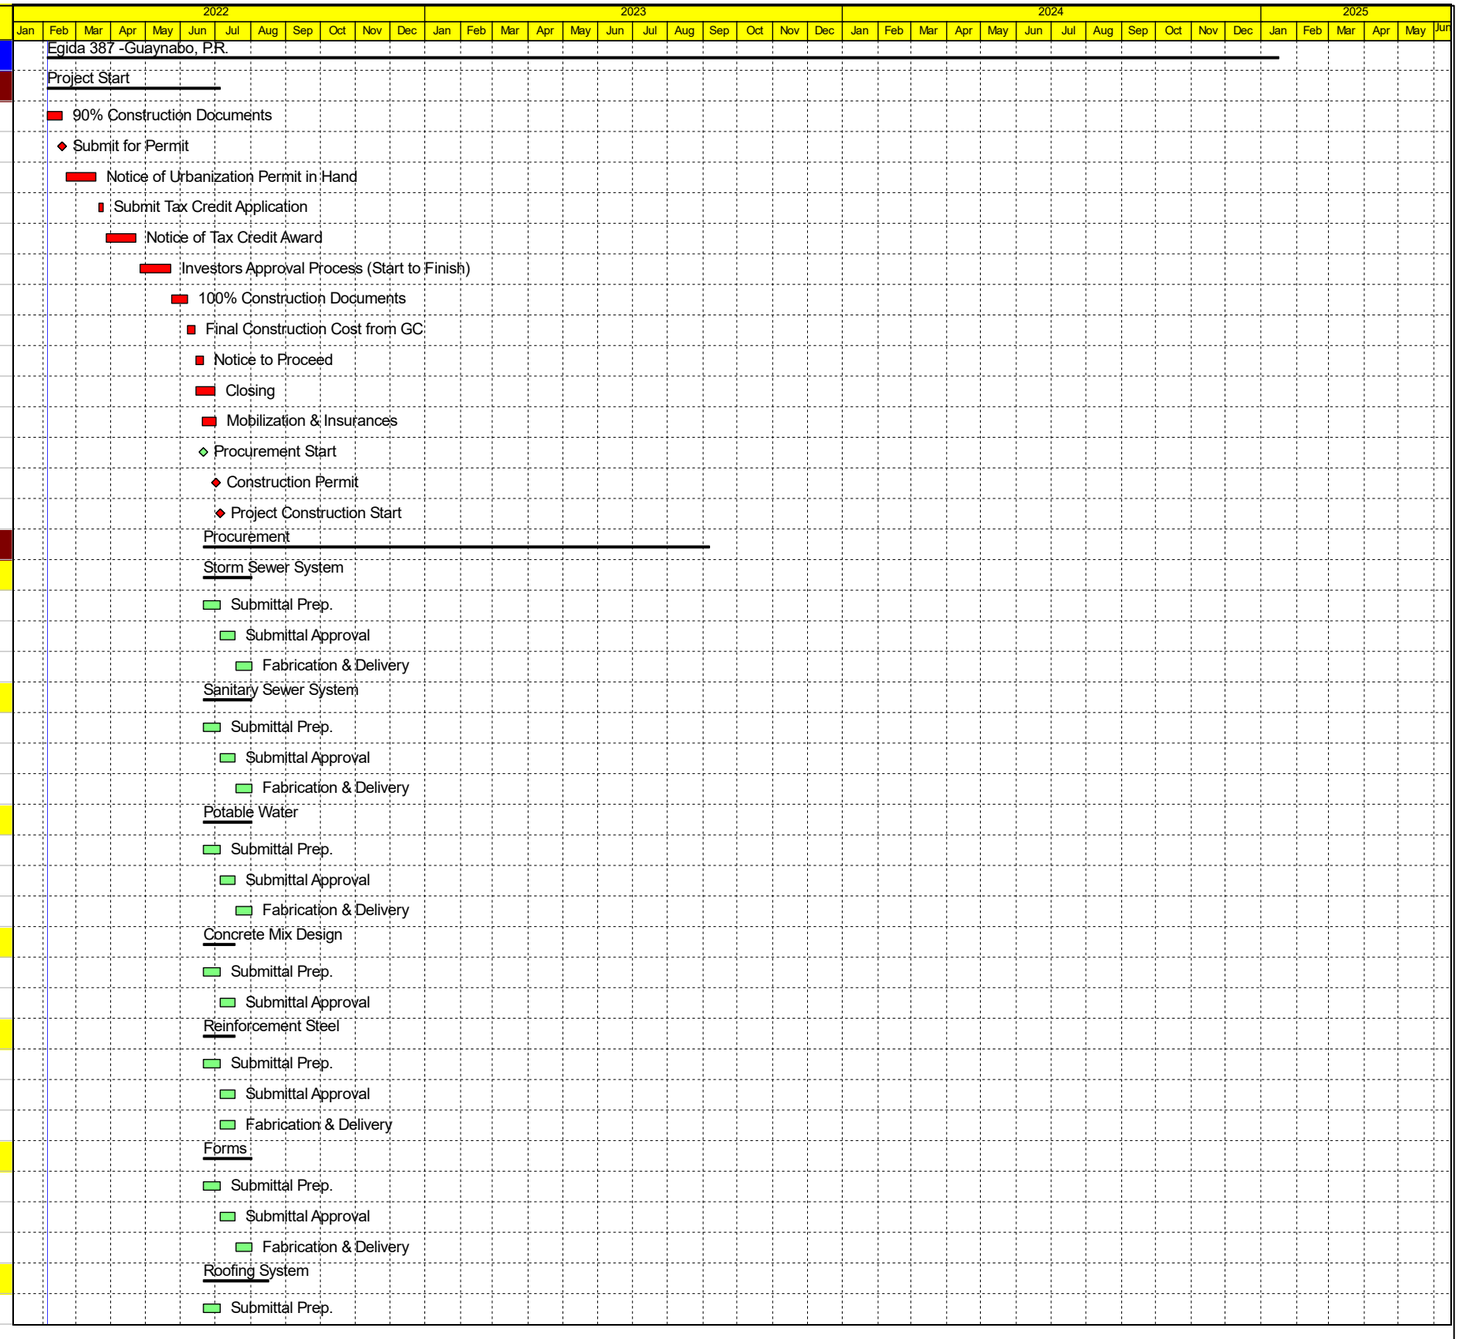


- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1175	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1180	Fabrication & Delivery	20	Jul-19-22	Aug-16-22
Doors & Hardware		71	Jun-21-22	Sep-27-22
CIC-1125	Submittal Prep.	20	Jun-21-22	Jul-19-22
CIC-1130	Submittal Approval	10	Jul-19-22	Aug-02-22
CIC-1135	Fabrication & Delivery	40	Aug-02-22	Sep-27-22
Windows		61	Jun-21-22	Sep-13-22
CIC-1140	Submittal Prep.	20	Jun-21-22	Jul-19-22
CIC-1145	Submittal Approval	10	Jul-19-22	Aug-02-22
CIC-1150	Fabrication & Delivery	30	Aug-02-22	Sep-13-22
Floorign System		56	Jun-21-22	Sep-06-22
CIC-1155	Submittal Prep.	15	Jun-21-22	Jul-12-22
CIC-1160	Submittal Approval	10	Jul-12-22	Jul-26-22
CIC-1165	Fabrication & Delivery	30	Jul-26-22	Sep-06-22
Paint		31	Jun-21-22	Aug-02-22
CIC-1185	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1190	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1195	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Elevators		153	Dec-19-22	Jul-19-23
CIC-1200	Submittal Prep.	20	Dec-19-22*	Jan-18-23
CIC-1205	Submittal Approval	10	Jan-16-23	Jan-27-23
CIC-1210	Fabrication & Delivery	120	Jan-30-23	Jul-19-23
Kitchens		133	Mar-06-23	Sep-06-23
CIC-4200	Submittal Prep.	20	Mar-06-23*	Mar-31-23
CIC-4205	Submittal Approval	10	Apr-03-23	Apr-17-23
CIC-4210	Fabrication & Delivery	100	Apr-17-23	Sep-06-23
Appliances		111	Jun-21-22	Nov-22-22
CIC-1335	Submittal Prep.	20	Jun-21-22	Jul-19-22
CIC-1340	Submittal Approval	10	Jul-19-22	Aug-02-22
CIC-1345	Fabrication & Delivery	80	Aug-02-22	Nov-22-22
HVAC & A/C		111	Jun-21-22	Nov-22-22
CIC-1110	Submittal Prep.	20	Jun-21-22	Jul-19-22
CIC-1115	Submittal Approval	10	Jul-19-22	Aug-02-22
CIC-1120	Fabrication & Delivery	80	Aug-02-22	Nov-22-22
Piping		31	Jun-21-22	Aug-02-22
CIC-1215	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1220	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1225	Fabrication & Delivery	10	Jul-19-22	Aug-02-22
Plumbing Fixtures		80	Jun-21-22	Oct-10-22
CIC-1230	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1235	Submittal Approval	10	Jul-05-22	Jul-18-22
CIC-1240	Fabrication & Delivery	60	Jul-19-22	Oct-10-22

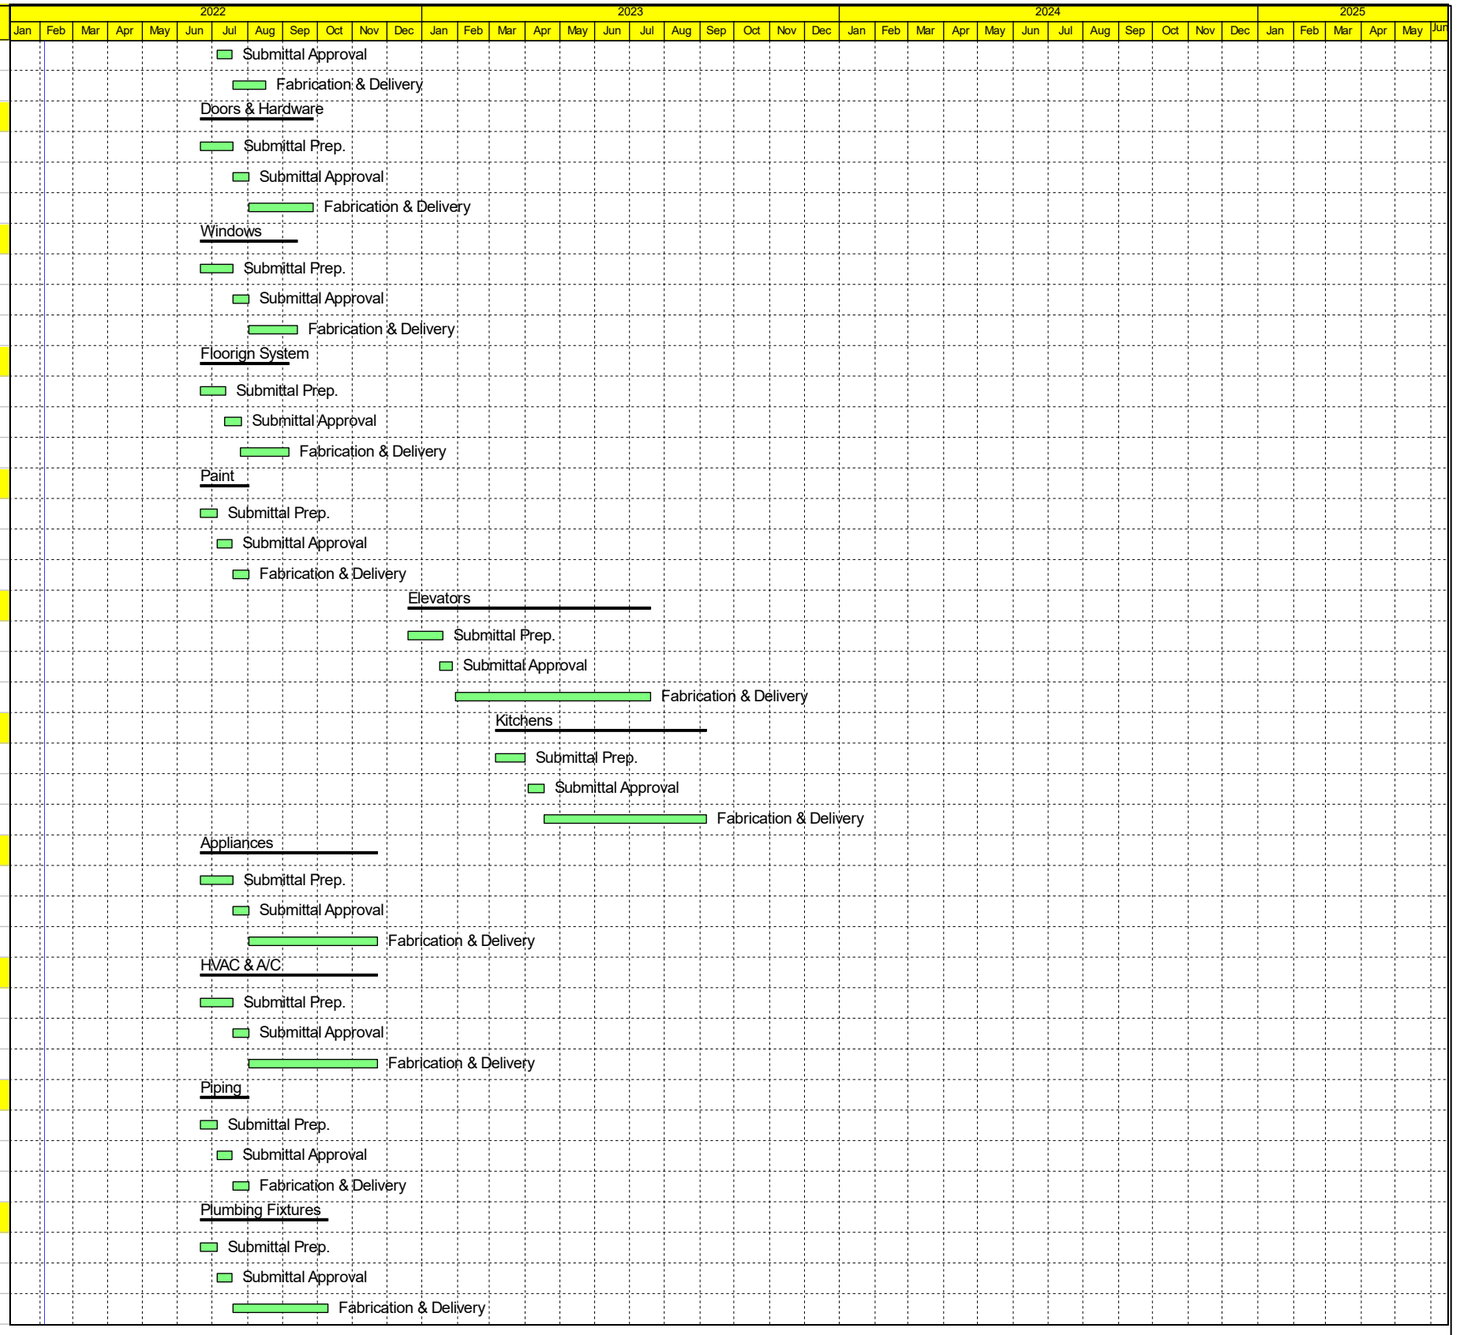

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
Conduits & Wiring		26	Jun-21-22	Jul-26-22
CIC-1245	Submittal Prep.	10	Jun-21-22	Jul-05-22
CIC-1250	Submittal Approval	10	Jun-28-22	Jul-12-22
CIC-1255	Fabrication & Delivery	10	Jul-12-22	Jul-26-22
Electrical Devices		155	Jun-21-22	Jan-23-23
CIC-1260	Submittal Prep.	20	Jun-21-22	Jul-19-22
CIC-1265	Submittal Approval	10	Jul-19-22	Aug-02-22
CIC-1270	Fabrication & Delivery	120	Aug-02-22	Jan-23-23
Construction		643	Jul-05-22	Dec-19-24
Site Work		627	Jul-05-22	Nov-27-24
CIC-1275	CES Plan Implementation	5	Jul-05-22	Jul-11-22
CIC-1280	Demolition	9	Jul-12-22	Jul-22-22
CIC-1420	Clearing & Grubbing	10	Jul-26-22	Aug-08-22
CIC-1315	Earthwork	39	Aug-09-22	Oct-03-22
CIC-1290	Underground Utilities	58	Oct-04-22	Dec-23-22
CIC-1295	Curbs & Gutters	20	Jun-27-24	Jul-24-24
CIC-1300	Sidewalks	20	Jul-25-24	Aug-21-24
CIC-1310	Pavements	40	Aug-22-24	Oct-16-24
CIC-1305	Fence Installation	15	Oct-17-24	Nov-06-24
CIC-1560	Landscaping	30	Oct-17-24	Nov-27-24
Building		578	Oct-04-22	Dec-19-24
Basement		552	Oct-04-22	Nov-13-24
Civil/Structural		111	Oct-04-22	Mar-07-23
CIC-1485	Cistern Excavation	5	Oct-04-22	Oct-10-22
CIC-1540	Cistern Matt Foundations	20	Oct-11-22	Nov-07-22
CIC-1555	Cistern Concrete Walls Rebar & Concrete Pour	10	Nov-08-22	Nov-21-22
CIC-1325	Foundations	19	Nov-08-22	Dec-05-22
CIC-4080	Cistern Waterproofing	4	Nov-22-22	Nov-28-22
CIC-4070	Cistern Top Slab Forms & Rebar	7	Nov-29-22	Dec-07-22
CIC-1425	Basement Concrete Slab Rebar & Forms	10	Dec-06-22	Dec-19-22
CIC-4075	Cistern Top Slab Concrete Pour	1	Dec-08-22	Dec-09-22
CIC-4085	Basement Concrete Slab Pour	5	Dec-14-22	Dec-20-22
CIC-1330	Basement Concrete Walls	17	Dec-21-22	Jan-17-23
CIC-1495	Backfill	15	Jan-18-23	Feb-07-23
CIC-1590	Concrete Stairs	20	Jan-18-23	Feb-14-23
CIC-1320	Utilities Installation	20	Feb-08-23	Mar-07-23
CIC-1445	Signs & Markings	10	Feb-15-23	Feb-28-23
Finishes		446	Mar-01-23	Nov-13-24
CIC-1061	Ceiling Cement Plaster	8	Mar-01-23	Mar-10-23
CIC-1062	Walls Cement Plaster	10	Mar-13-23	Mar-24-23
CIC-1076	Ceiling Exhaust Fan Duct	3	Mar-27-23	Mar-29-23
CIC-1067	Cistern & Elevator Pit Waterproofing Installation	5	Mar-27-23	Mar-31-23

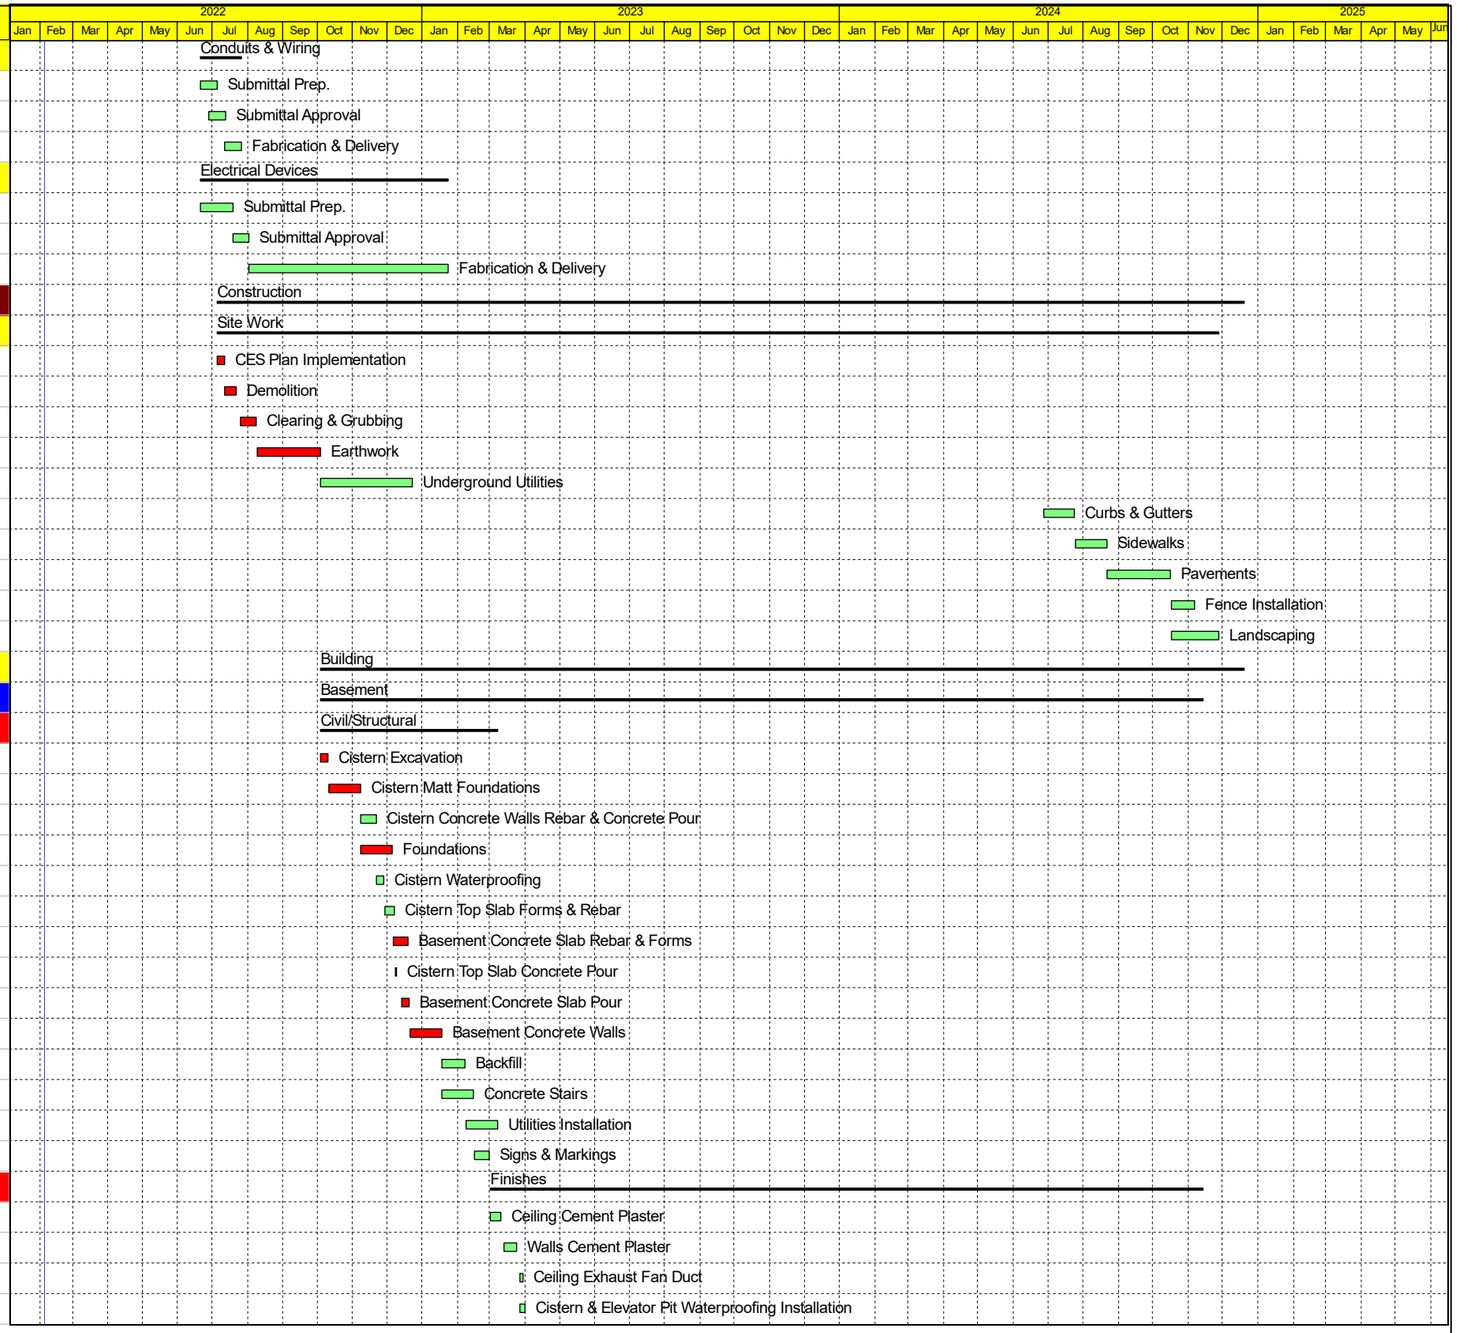

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1082	Swing Door Installation	5	Mar-27-23	Mar-31-23
CIC-1600	Floor Topping	5	Mar-27-23	Mar-31-23
CIC-1084	Stairs Railings Installation	8	Mar-27-23	Apr-05-23
CIC-1063	Fire Protection Pump Installation	9	Mar-27-23	Apr-06-23
CIC-1064	PW Pump Installation	9	Mar-27-23	Apr-06-23
CIC-1620	Fire Protection Piping	9	Mar-27-23	Apr-06-23
CIC-1078	Ceiling Exhaust Fan & Diffuser Installation	5	Mar-30-23	Apr-05-23
CIC-1630	Paint Doors	4	Apr-03-23	Apr-06-23
CIC-1094	Paint - Ceiling & Walls Finish Coat	4	Apr-06-23	Apr-12-23
CIC-1071	Fire Protection Test	2	Apr-10-23	Apr-11-23
CIC-1091	Doors Hardware Installation	5	Apr-10-23	Apr-14-23
CIC-1066	Fire Protection Sprinklers Installation	5	Apr-12-23	Apr-18-23
CIC-1093	Wiring Devices	2	Apr-13-23	Apr-14-23
CIC-1088	Cameras Installation	5	Apr-13-23	Apr-19-23
CIC-1089	Intercom System Installation	5	Apr-13-23	Apr-19-23
CIC-1725	Substantial Completion	0		Apr-19-23
CIC-1726	Punch List	20	Apr-20-23	May-17-23
CIC-1565	Elevators Installation	80	Jul-25-24	Nov-13-24
Ground Floor		180	Jan-18-23	Sep-26-23
Civil/Structural		100	Jan-18-23	Jun-06-23
CIC-1350	Ground Level Concrete Slab	20	Jan-18-23	Feb-14-23
CIC-1355	Ground Level Concrete Walls	30	Feb-15-23	Mar-28-23
CIC-1450	CMU Installation Ground Floor	29	Apr-26-23	Jun-06-23
CIC-1103	Concrete Stairs FRP	10	May-03-23	May-16-23
Finishes		85	May-31-23	Sep-26-23
CIC-4095	Electrical Rough In (Lighting, Power, Communications & Intercome	5	May-31-23	Jun-06-23
CIC-4105	San. Sewer, PW & Storm Sewer Piping Rough In	5	May-31-23	Jun-06-23
CIC-4115	Fire Protection Rough In	2	Jun-05-23	Jun-06-23
CIC-1117	Cement Plaster Ceiling	8	Jun-07-23	Jun-16-23
CIC-1118	Cement Plaster Walls	10	Jun-15-23	Jun-28-23
CIC-1121	Topping Installation	4	Jun-29-23	Jul-05-23
CIC-1123	Stair Railings	5	Jun-29-23	Jul-06-23
CIC-1203	Fire Protection Piping	9	Jun-29-23	Jul-12-23
CIC-1119	Window, Glass & Louver Installation	11	Jun-29-23	Jul-14-23
CIC-1124	Courtyard Flooring	5	Jul-06-23	Jul-12-23
CIC-1735	GB Installation	6	Jul-06-23	Jul-13-23
CIC-1126	Floor Tile Installation	10	Jul-11-23	Jul-24-23
CIC-1144	Fire Protection Test	2	Jul-13-23	Jul-14-23
CIC-1127	Base Tile Waterproofing	5	Jul-14-23*	Jul-20-23
CIC-1740	Ceiling & Wall Primert & 1st Coat	10	Jul-14-23	Jul-27-23
CIC-1204	Fire Protection Sprinklers	5	Jul-17-23	Jul-21-23
CIC-1129	Entrance Doors Installation	3	Jul-18-23	Jul-20-23

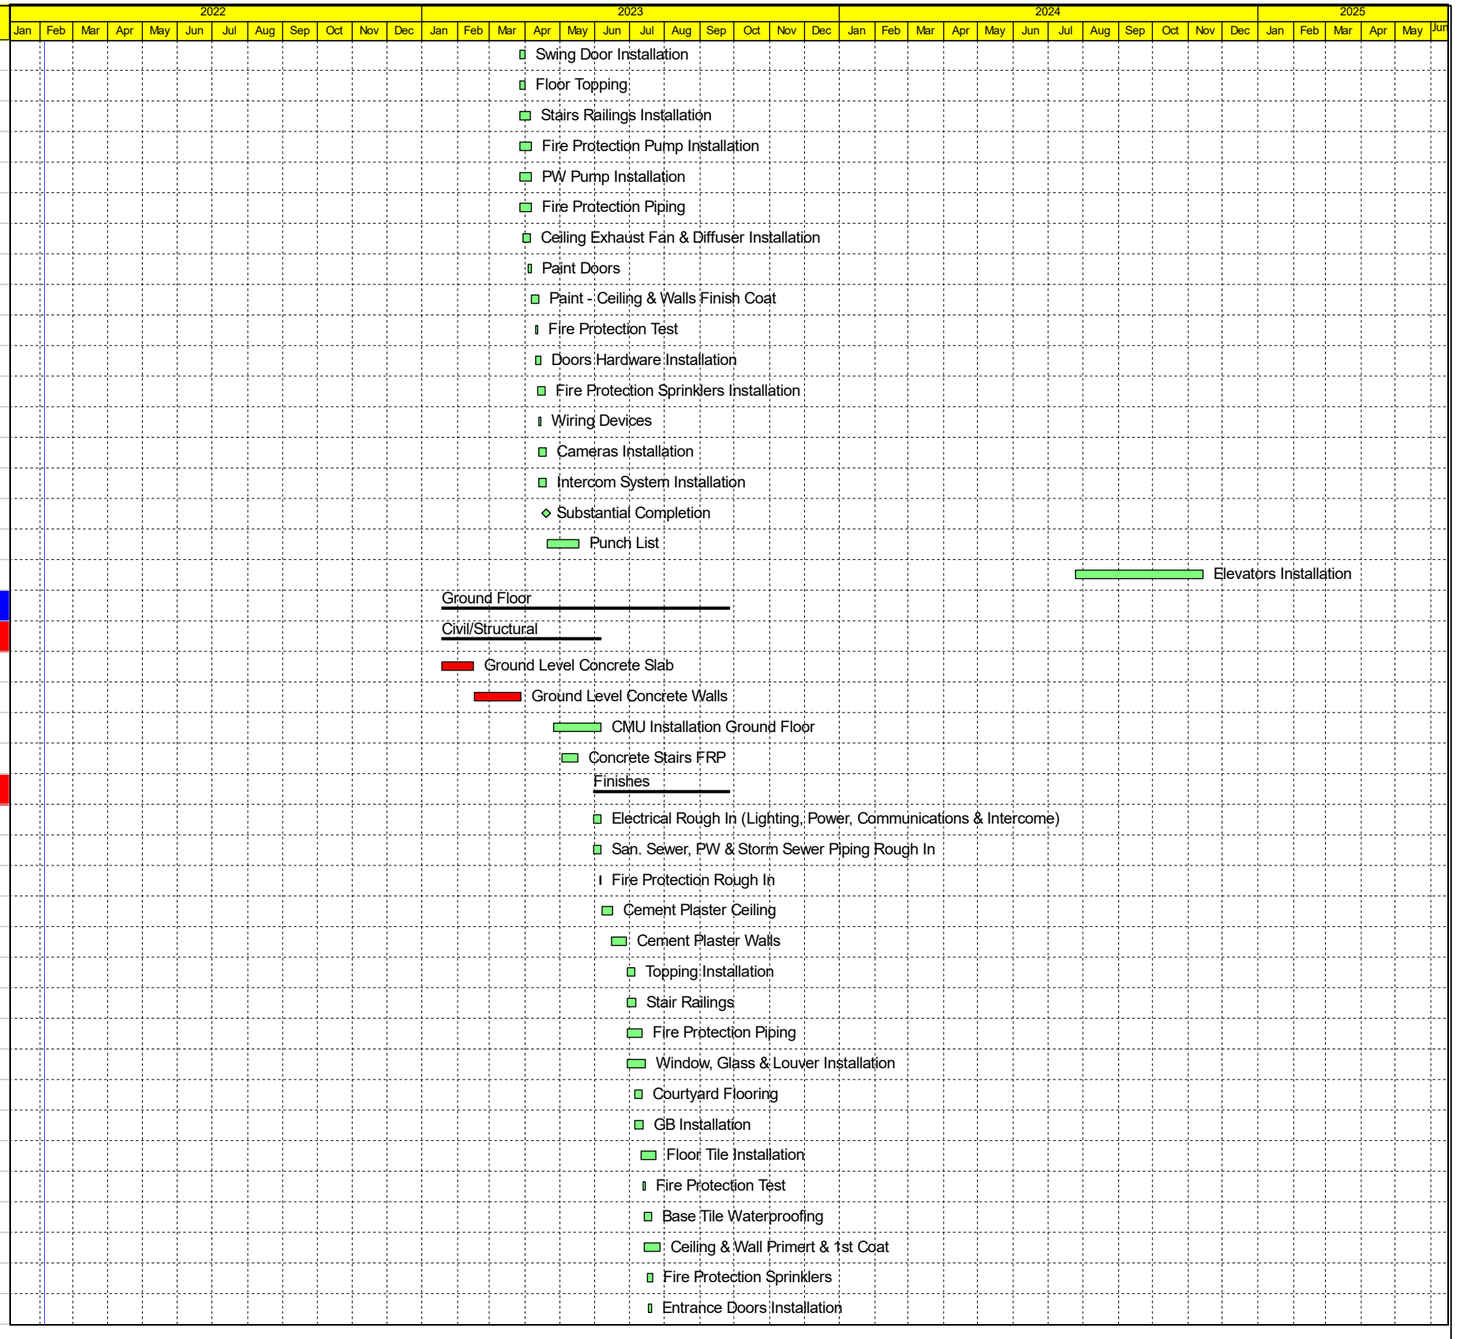

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1745	Courtyard Planters	5	Jul-18-23	Jul-24-23
CIC-1755	Interior Wood Door Installation	6	Jul-21-23*	Jul-28-23
CIC-1750	Cabinets Installation	4	Jul-24-23*	Jul-27-23
CIC-1128	Wall Tile Installation	3	Jul-25-23	Jul-27-23
CIC-1133	Hollow Metal Doors Installation	6	Jul-25-23*	Aug-01-23
CIC-1137	Wiring Devices	4	Jul-28-23	Aug-02-23
CIC-1141	Plumbing Fixtures	4	Jul-28-23	Aug-02-23
CIC-1760	Intercom System Installation	4	Jul-28-23	Aug-02-23
CIC-1138	Exhaust Fan Ducts & Diffusers Installation	5	Jul-28-23*	Aug-03-23
CIC-1650	Fire Alarm System Cabinet Installation	10	Jul-28-23	Aug-10-23
CIC-1136	Doors Paint	6	Aug-02-23	Aug-09-23
CIC-1134	Doors Hardware Installation	4	Aug-09-23	Aug-14-23
CIC-1142	Electrical Panel Installation	4	Aug-09-23	Aug-14-23
CIC-1148	Ceiling & Wall Paint Finish Coat	8	Aug-09-23	Aug-18-23
CIC-1143	Electrical Rooms Meterbanks Installation	3	Aug-10-23	Aug-14-23
CIC-1086	Electrical Generator Installation	10	Aug-15-23	Aug-28-23
CIC-1087	Substation Installation	10	Aug-15-23	Aug-28-23
CIC-1146	Bathroom Accessories	3	Aug-16-23	Aug-18-23
CIC-1147	New Appliances	2	Aug-17-23*	Aug-18-23
CIC-1727	Substantial Completion	0		Aug-28-23
CIC-1728	Punch List	20	Aug-29-23	Sep-26-23
2nd Floor		177	Mar-29-23	Nov-30-23
Civil/Structural		100	Mar-29-23	Aug-15-23
CIC-1360	2nd Level Concrete Slab	19	Mar-29-23	Apr-25-23
CIC-1365	2nd Level Concrete Walls	29	Apr-26-23	Jun-06-23
CIC-1455	CMU Installation 2nd Floor	30	Jul-05-23	Aug-15-23
CIC-1157	Concrete Stairs FRP	10	Jul-12-23	Jul-25-23
Finishes		77	Aug-16-23	Nov-30-23
CIC-1770	Fire Protection Rough In	2	Aug-16-23	Aug-17-23
CIC-1780	Fire Pump Exhaust Installation	3	Aug-16-23	Aug-18-23
CIC-1162	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Aug-16-23	Aug-22-23
CIC-1164	San. Sewer, PW & Storm Sewer Piping Rough In	5	Aug-16-23	Aug-22-23
CIC-1168	Apartment Exhaust Duct Installation	8	Aug-16-23	Aug-25-23
CIC-1171	Cement Plaster Ceiling	8	Aug-16-23	Aug-25-23
CIC-1172	Cement Plaster Walls	11	Aug-24-23	Sep-08-23
CIC-1201	Fire Protection Piping	9	Aug-28-23	Sep-08-23
CIC-1202	Fire Protection Test	2	Sep-11-23	Sep-12-23
CIC-1790	Topping Installation	5	Sep-11-23	Sep-15-23
CIC-1177	Stair Railings	6	Sep-11-23	Sep-18-23
CIC-1173	Window, Glass & Louver Installation	10	Sep-11-23	Sep-22-23
CIC-1163	Fire Protection Sprinklers	5	Sep-13-23	Sep-19-23
CIC-1176	Shower Base	3	Sep-18-23	Sep-20-23

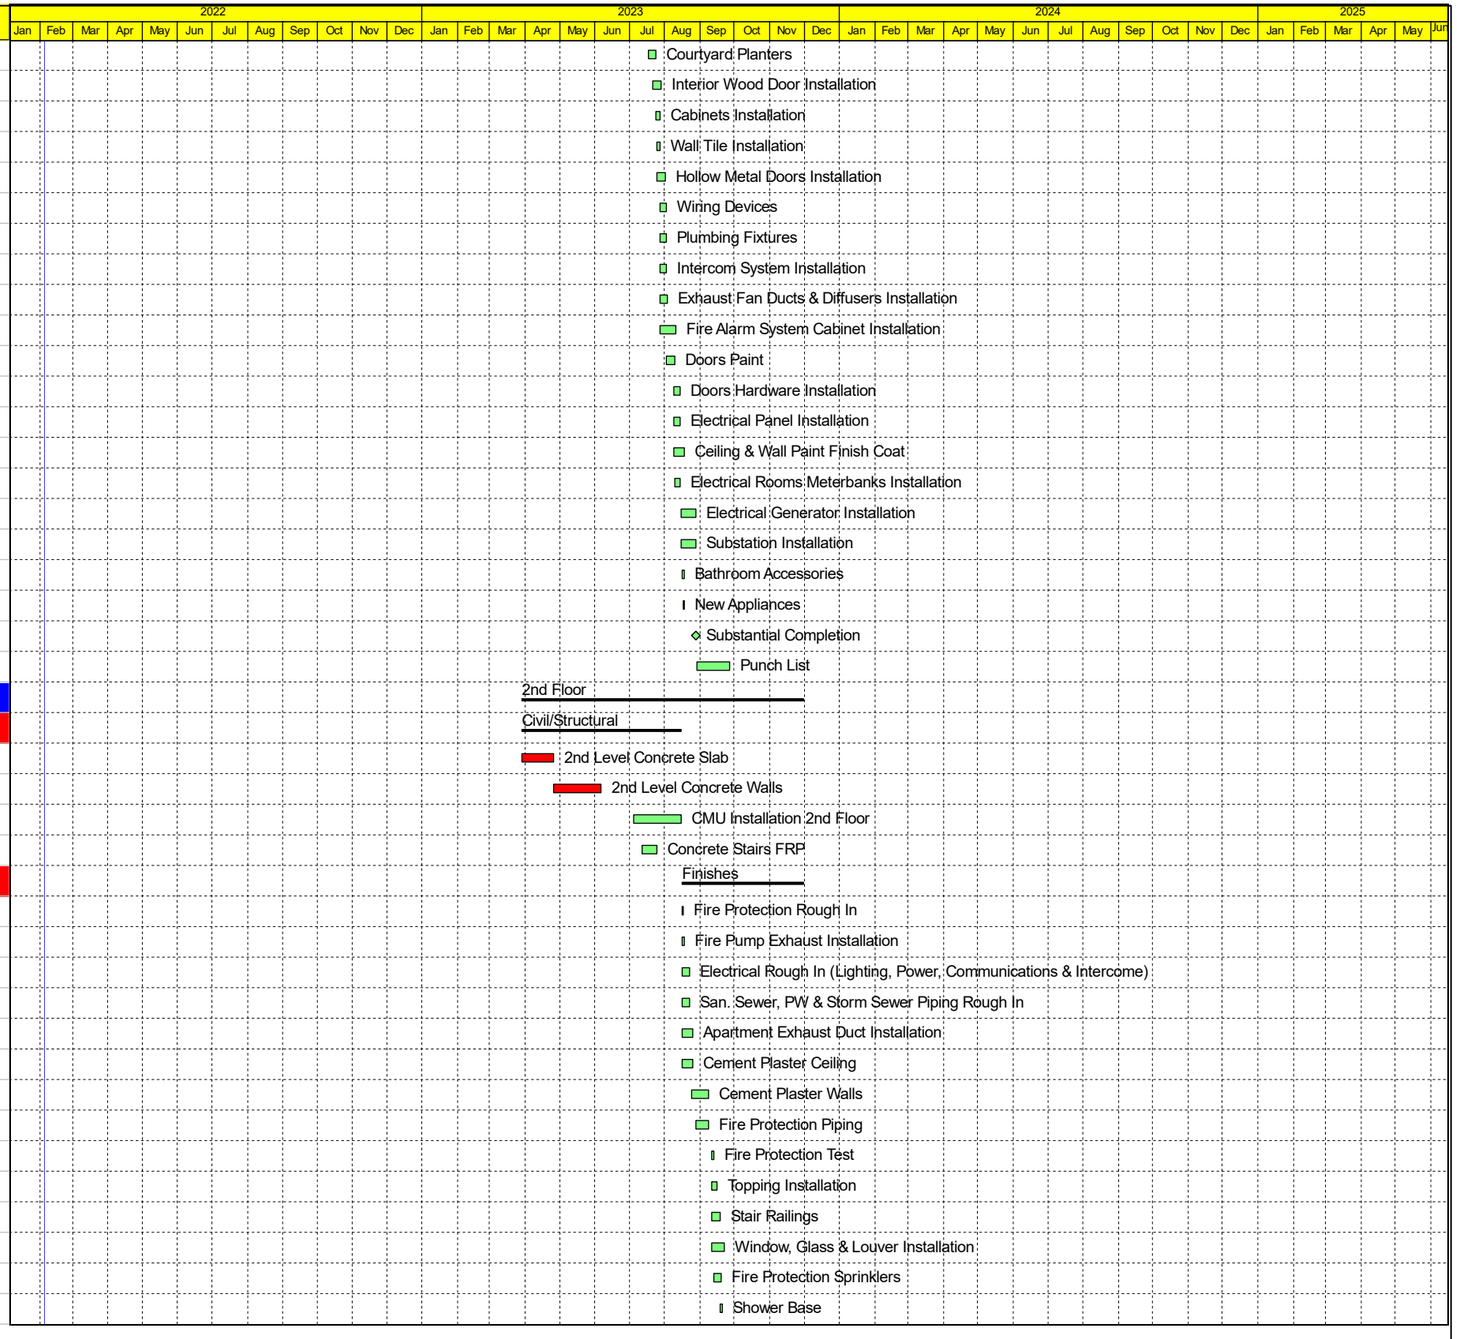

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1178	Terrace Tile Water Proofing	5	Sep-18-23	Sep-22-23
CIC-1174	GB Installation	10	Sep-18-23	Sep-29-23
CIC-1800	Floor Tile Installation	10	Sep-21-23	Oct-04-23
CIC-1179	Terrace Railings	5	Sep-28-23	Oct-04-23
CIC-1810	Sliding Doors Installation	8	Sep-28-23	Oct-09-23
CIC-1181	Base Tile Waterproofing	5	Oct-02-23	Oct-06-23
CIC-1189	Ceiling & Wall Primert & 1st Coat	12	Oct-02-23	Oct-17-23
CIC-1184	Interior Wood Door Installation	12	Oct-04-23	Oct-19-23
CIC-1187	Hollow Metal Doors Installation	4	Oct-05-23	Oct-10-23
CIC-1183	Entrance Doors Installation	5	Oct-05-23	Oct-11-23
CIC-1186	Closet Mirror Doors Installation	8	Oct-10-23	Oct-19-23
CIC-1193	Kitchen Installation	8	Oct-10-23	Oct-19-23
CIC-1182	Wall Tile Installation	6	Oct-12-23	Oct-19-23
CIC-1820	Doors Paint	10	Oct-12-23	Oct-25-23
CIC-1198	Intercom System Installation	4	Oct-18-23	Oct-23-23
CIC-1191	Wiring Devices	8	Oct-18-23	Oct-27-23
CIC-1194	Plumbing Fixtures	8	Oct-18-23	Oct-27-23
CIC-1188	Doors Hardware Installation	8	Oct-19-23	Oct-30-23
CIC-1830	Apartments Electrical Panel Installation	8	Oct-19-23	Oct-30-23
CIC-1197	Ceiling & Wall Paint Finish Coat	10	Oct-19-23	Nov-01-23
CIC-1192	Apartments Exhaust Fan Diffuser Installation	8	Oct-20-23	Oct-31-23
CIC-1199	Bathroom Accessories	6	Oct-25-23	Nov-01-23
CIC-1196	Electrical Rooms Meterbanks Installation	3	Oct-26-23	Oct-30-23
CIC-1840	New Appliances	4	Oct-27-23	Nov-01-23
CIC-1729	Substantial Completion	0		Nov-01-23
CIC-1850	Punch List	20	Nov-02-23	Nov-30-23
3rd Floor		176	Jun-07-23	Feb-07-24
Civil/Structural		100	Jun-07-23	Oct-24-23
CIC-1370	3rd Level Concrete Slab	19	Jun-07-23	Jul-03-23
CIC-1375	3rd Level Concrete Walls	30	Jul-05-23	Aug-15-23
CIC-1460	CMU Installation 3rd Floor	30	Sep-13-23	Oct-24-23
CIC-1213	Concrete Stairs FRP	10	Sep-20-23	Oct-03-23
Finishes		76	Oct-25-23	Feb-07-24
CIC-1221	Fire Protection Rough In	2	Oct-25-23	Oct-26-23
CIC-1226	Fire Pump Exhaust Installation	3	Oct-25-23	Oct-27-23
CIC-1218	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Oct-25-23	Oct-31-23
CIC-1860	San. Sewer, PW & Storm Sewer Piping Rough In	5	Oct-25-23	Oct-31-23
CIC-1224	Apartment Exhaust Duct Installation	8	Oct-25-23	Nov-03-23
CIC-1227	Cement Plaster Ceiling	8	Oct-25-23	Nov-03-23
CIC-1228	Cement Plaster Walls	12	Nov-02-23	Nov-17-23
CIC-1257	Fire Protection Piping	10	Nov-06-23	Nov-17-23
CIC-1258	Fire Protection Test	2	Nov-20-23	Nov-21-23

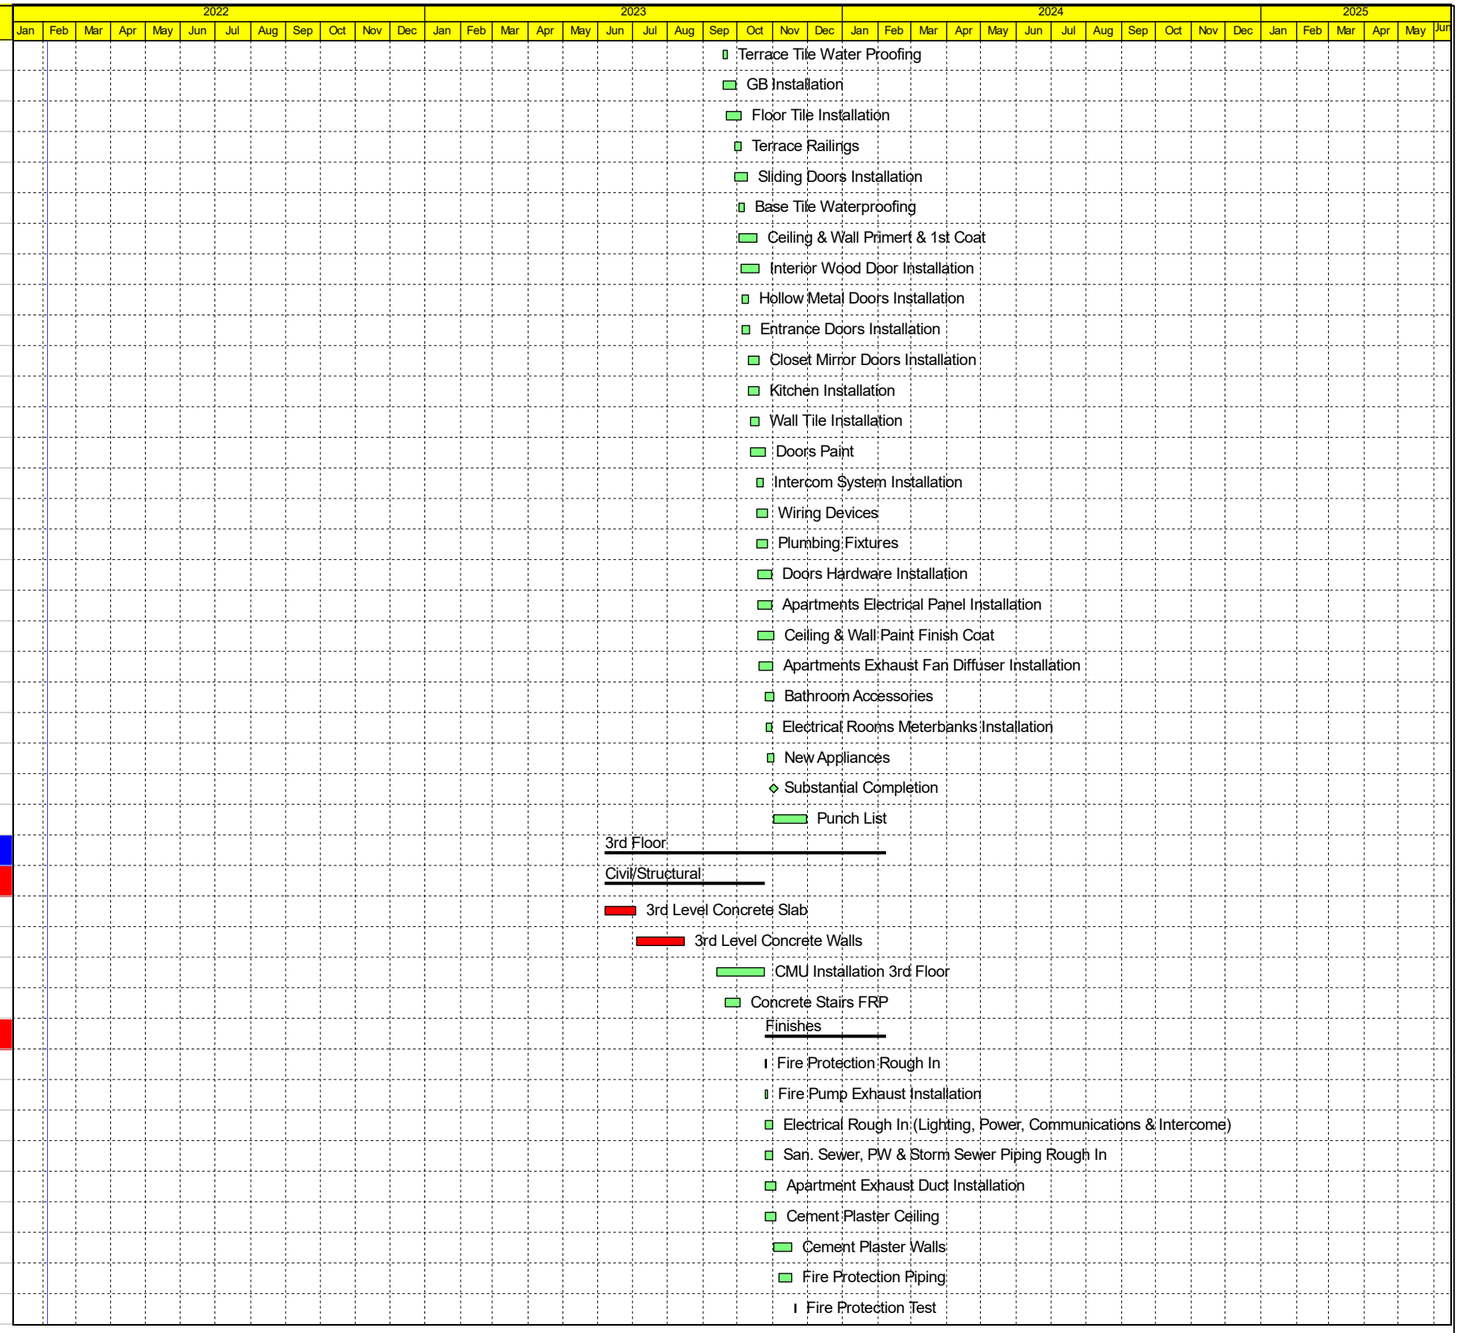


- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.
CIC Construction Group, S.E.
Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1231	Topping Installation	4	Nov-20-23	Nov-24-23
CIC-1233	Stair Railings	5	Nov-20-23	Nov-27-23
CIC-1229	Window, Glass & Louver Installation	9	Nov-20-23	Dec-01-23
CIC-1219	Fire Protection Sprinklers	4	Nov-22-23	Nov-28-23
CIC-1232	Shower Base	3	Nov-27-23	Nov-29-23
CIC-1234	Terrace Tile Water Proofing	5	Nov-27-23	Dec-01-23
CIC-1870	GB Installation	10	Nov-27-23	Dec-08-23
CIC-1236	Floor Tile Installation	10	Nov-30-23	Dec-13-23
CIC-1880	Terrace Railings	5	Dec-07-23	Dec-13-23
CIC-1241	Sliding Doors Installation	8	Dec-07-23	Dec-18-23
CIC-1237	Base Tile Waterproofing	5	Dec-11-23	Dec-15-23
CIC-1890	Ceiling & Wall Primert & 1st Coat	11	Dec-11-23	Dec-26-23
CIC-1900	Interior Wood Door Installation	11	Dec-13-23	Dec-28-23
CIC-1243	Hollow Metal Doors Installation	4	Dec-14-23	Dec-19-23
CIC-1239	Entrance Doors Installation	5	Dec-14-23	Dec-20-23
CIC-1242	Closet Mirror Doors Installation	7	Dec-19-23	Dec-28-23
CIC-1249	Kitchen Installation	7	Dec-19-23	Dec-28-23
CIC-1238	Wall Tile Installation	5	Dec-21-23	Dec-28-23
CIC-1246	Doors Paint	8	Dec-21-23	Jan-03-24
CIC-1254	Intercom System Installation	3	Dec-27-23	Dec-29-23
CIC-1247	Wiring Devices	7	Dec-27-23	Jan-05-24
CIC-1910	Plumbing Fixtures	7	Dec-27-23	Jan-05-24
CIC-1244	Doors Hardware Installation	7	Dec-28-23	Jan-08-24
CIC-1251	Apartments Electrical Panel Installation	7	Dec-28-23	Jan-08-24
CIC-1253	Ceiling & Wall Paint Finish Coat	9	Dec-28-23	Jan-10-24
CIC-1248	Apartments Exhaust Fan Diffuser Installation	7	Dec-29-23	Jan-09-24
CIC-1920	Bathroom Accessories	6	Jan-03-24	Jan-10-24
CIC-1252	Electrical Rooms Meterbanks Installation	3	Jan-04-24	Jan-08-24
CIC-1256	New Appliances	4	Jan-05-24	Jan-10-24
CIC-1731	Substantial Completion	0		Jan-10-24
CIC-1732	Punch List	20	Jan-11-24	Feb-07-24
4th Floor		176	Aug-16-23	Apr-17-24
Civil/Structural		100	Aug-16-23	Jan-02-24
CIC-1380	4th Level Concrete Slab	19	Aug-16-23	Sep-12-23
CIC-1385	4th Level Concrete Walls	30	Sep-13-23	Oct-24-23
CIC-1465	CMU Installation 4th Floor	27	Nov-22-23	Jan-02-24
CIC-1960	Concrete Stairs FRP	10	Nov-29-23	Dec-12-23
Finishes		76	Jan-03-24	Apr-17-24
CIC-1950	Fire Protection Rough In	2	Jan-03-24	Jan-04-24
CIC-1980	Fire Pump Exhaust Installation	3	Jan-03-24	Jan-05-24
CIC-1930	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Jan-03-24	Jan-09-24
CIC-1940	San. Sewer, PW & Storm Sewer Piping Rough In	5	Jan-03-24	Jan-09-24

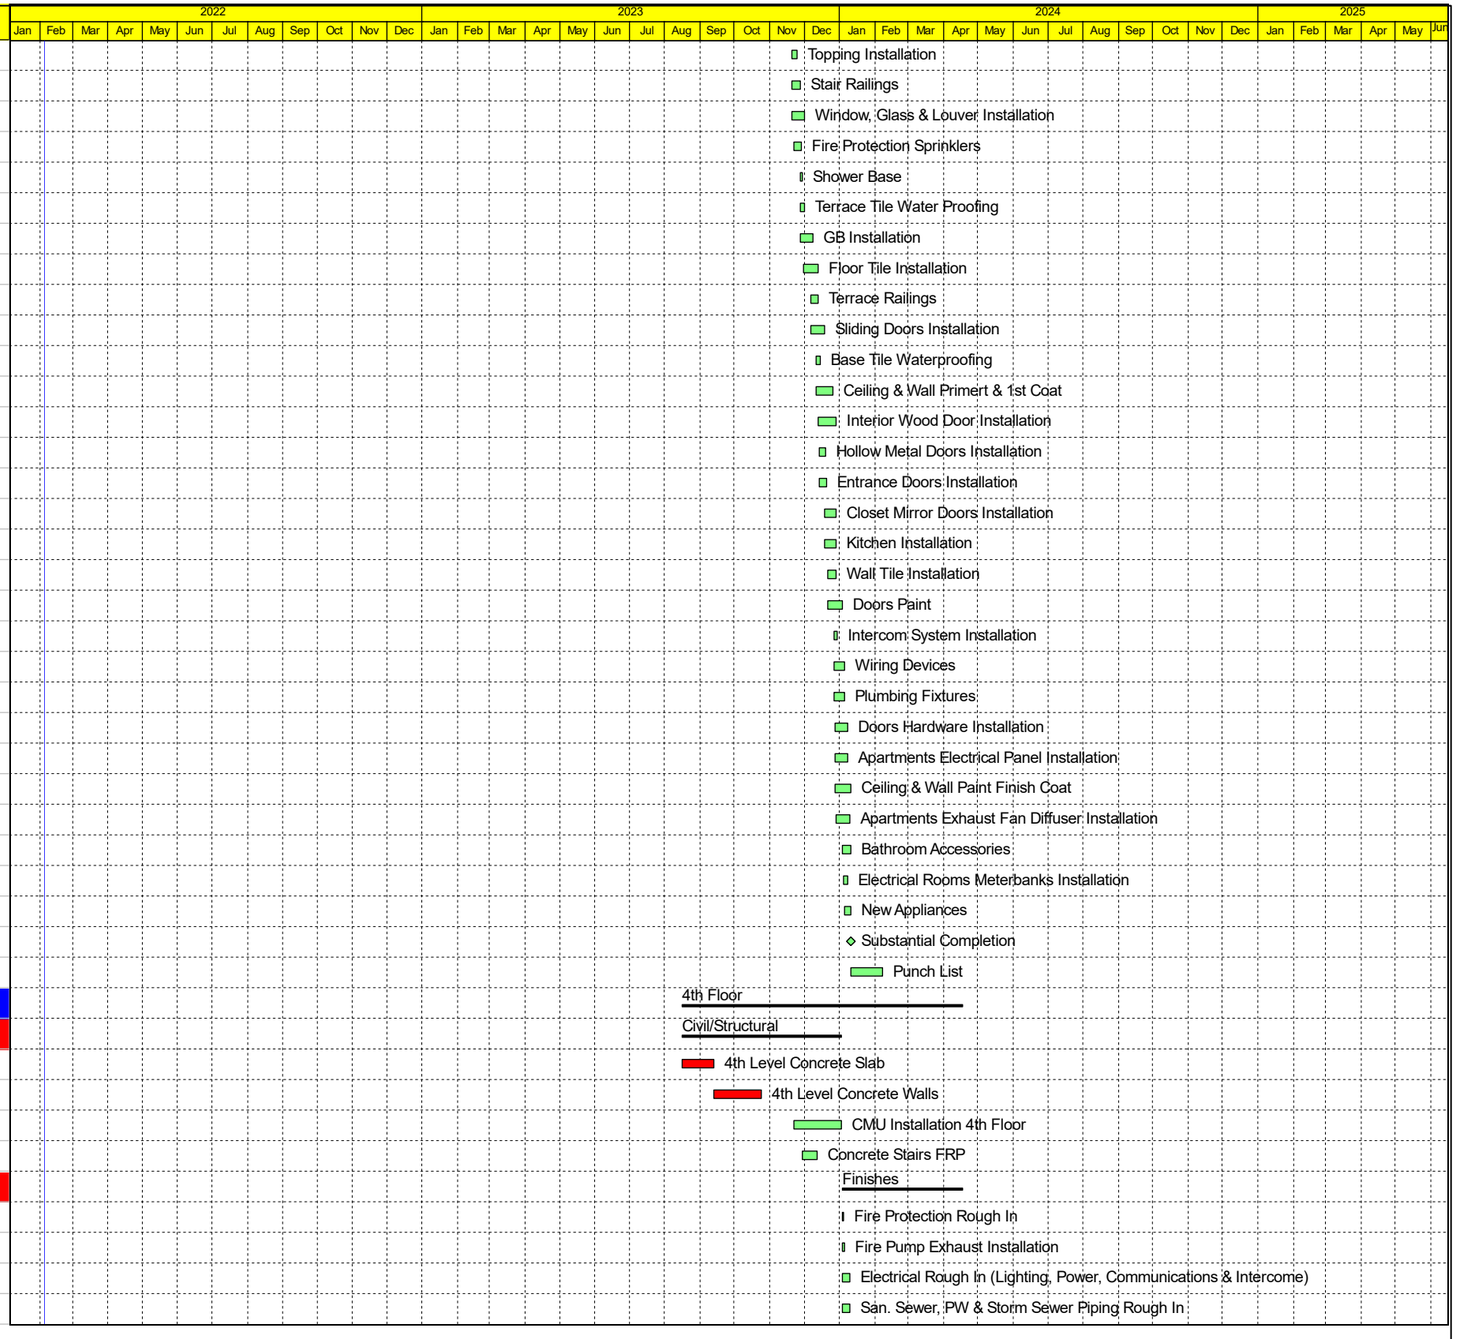

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-1970	Apartment Exhaust Duct Installation	8	Jan-03-24	Jan-12-24
CIC-1990	Cement Plaster Ceiling	8	Jan-03-24	Jan-12-24
CIC-2000	Cement Plaster Walls	12	Jan-11-24	Jan-26-24
CIC-2010	Fire Protection Piping	10	Jan-15-24	Jan-26-24
CIC-2020	Fire Protection Test	2	Jan-29-24	Jan-30-24
CIC-2030	Topping Installation	5	Jan-29-24	Feb-02-24
CIC-2040	Stair Railings	6	Jan-29-24	Feb-05-24
CIC-2050	Window, Glass & Louver Installation	10	Jan-29-24	Feb-09-24
CIC-2060	Fire Protection Sprinklers	5	Jan-31-24	Feb-06-24
CIC-2070	Shower Base	3	Feb-05-24	Feb-07-24
CIC-2080	Terrace Tile Water Proofing	5	Feb-05-24	Feb-09-24
CIC-2090	GB Installation	10	Feb-05-24	Feb-16-24
CIC-2100	Floor Tile Installation	10	Feb-08-24	Feb-21-24
CIC-2110	Terrace Railings	5	Feb-15-24	Feb-21-24
CIC-2120	Sliding Doors Installation	8	Feb-15-24	Feb-26-24
CIC-2130	Base Tile Waterproofing	5	Feb-19-24	Feb-23-24
CIC-2140	Ceiling & Wall Primert & 1st Coat	12	Feb-19-24	Mar-05-24
CIC-2150	Interior Wood Door Installation	12	Feb-21-24	Mar-07-24
CIC-2160	Hollow Metal Doors Installation	4	Feb-22-24	Feb-27-24
CIC-2170	Entrance Doors Installation	5	Feb-22-24	Feb-28-24
CIC-2180	Closet Mirror Doors Installation	8	Feb-27-24	Mar-07-24
CIC-2190	Kitchen Installation	8	Feb-27-24	Mar-07-24
CIC-2200	Wall Tile Installation	6	Feb-29-24	Mar-07-24
CIC-2210	Doors Paint	10	Feb-29-24	Mar-13-24
CIC-2220	Intercom System Installation	4	Mar-06-24	Mar-11-24
CIC-2230	Wiring Devices	8	Mar-06-24	Mar-15-24
CIC-2240	Plumbing Fixtures	8	Mar-06-24	Mar-15-24
CIC-2250	Doors Hardware Installation	8	Mar-07-24	Mar-18-24
CIC-2260	Apartments Electrical Panel Installation	8	Mar-07-24	Mar-18-24
CIC-2270	Ceiling & Wall Paint Finish Coat	10	Mar-07-24	Mar-20-24
CIC-2280	Apartments Exhaust Fan Diffuser Installation	8	Mar-08-24	Mar-19-24
CIC-2290	Bathroom Accessories	6	Mar-13-24	Mar-20-24
CIC-2300	Electrical Rooms Meterbanks Installation	3	Mar-14-24	Mar-18-24
CIC-2310	New Appliances	4	Mar-15-24	Mar-20-24
CIC-2320	Substantial Completion	0		Mar-20-24
CIC-2330	Punch List	20	Mar-21-24	Apr-17-24
5th Floor		176	Oct-25-23	Jun-26-24
Civil/Structural		100	Oct-25-23	Mar-12-24
CIC-1390	5th Level Concrete Slab	20	Oct-25-23	Nov-21-23
CIC-1395	5th Level Concrete Walls	27	Nov-22-23	Jan-02-24
CIC-1470	CMU Installation 5th Floor	30	Jan-31-24	Mar-12-24
CIC-2370	Concrete Stairs FRP	10	Feb-07-24	Feb-20-24

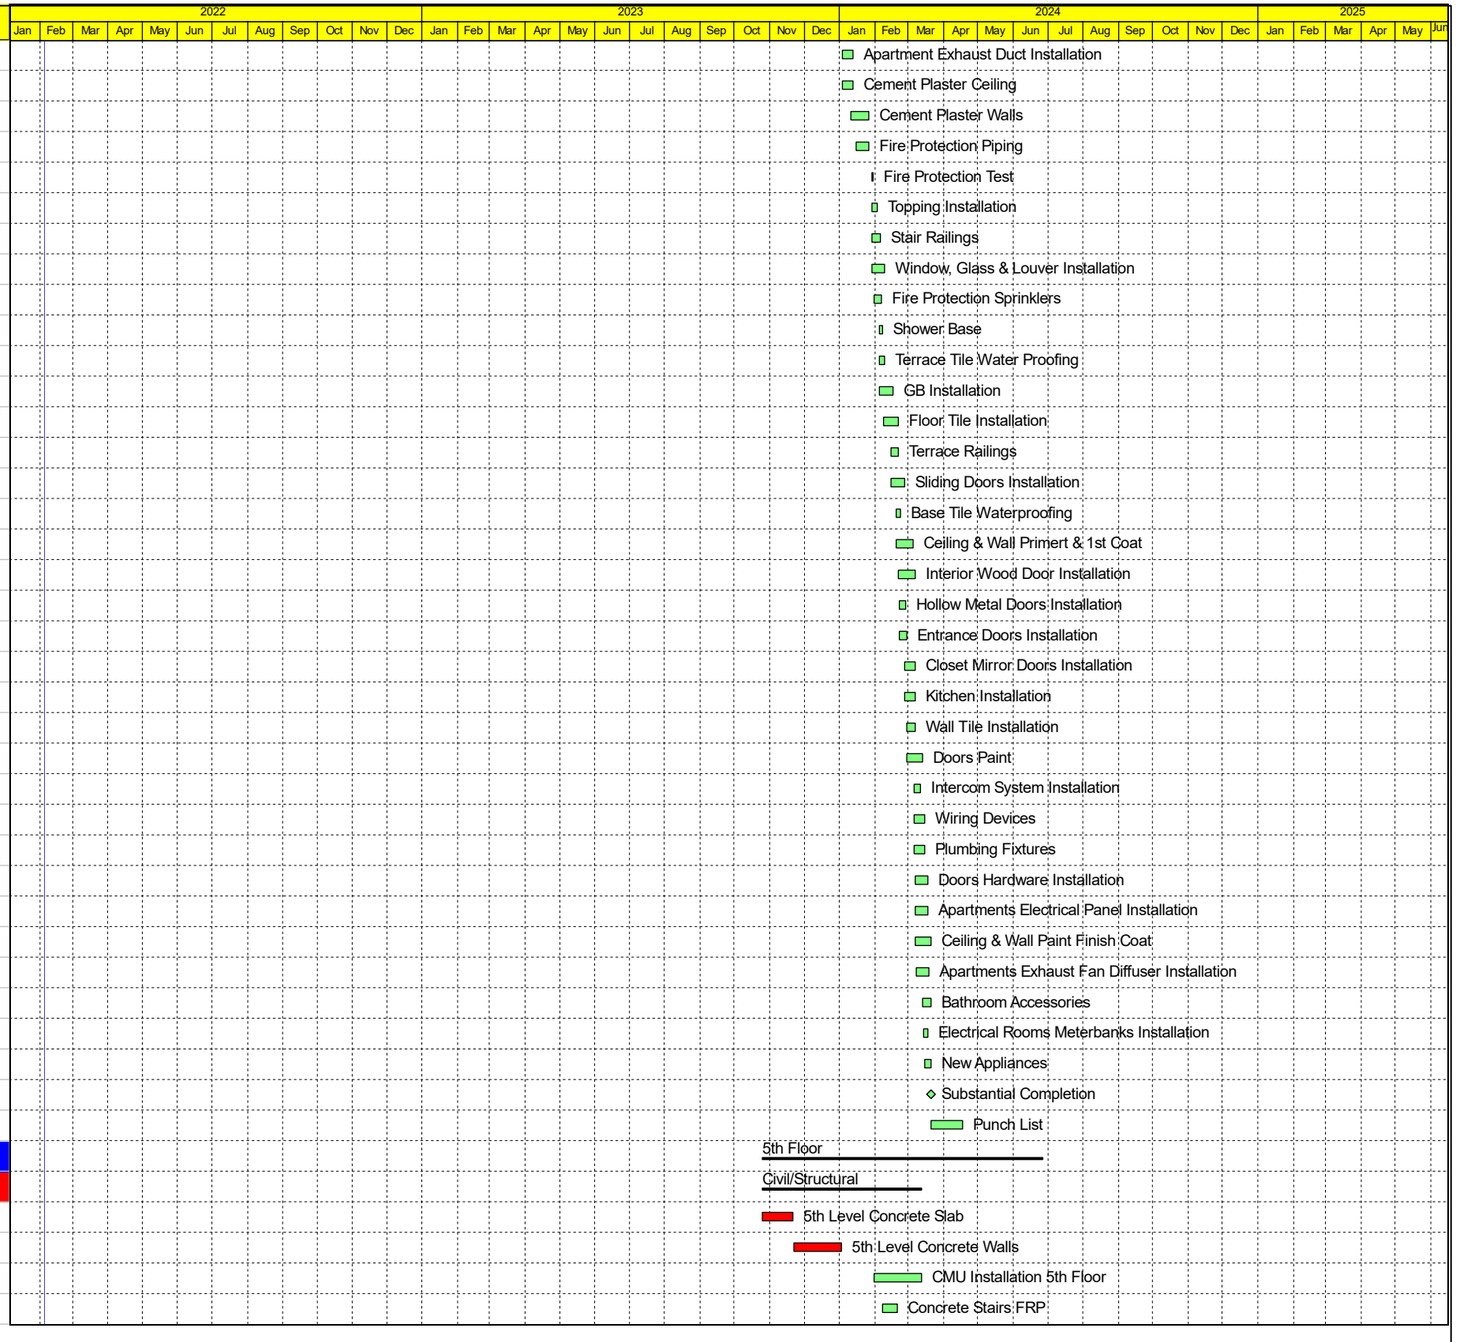


- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.
CIC Construction Group, S.E.
Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
Finishes		76	Mar-13-24	Jun-26-24
CIC-2360	Fire Protection Rough In	2	Mar-13-24	Mar-14-24
CIC-2390	Fire Pump Exhaust Installation	3	Mar-13-24	Mar-15-24
CIC-2340	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Mar-13-24	Mar-19-24
CIC-2350	San. Sewer, PW & Storm Sewer Piping Rough In	5	Mar-13-24	Mar-19-24
CIC-2380	Apartment Exhaust Duct Installation	8	Mar-13-24	Mar-22-24
CIC-2400	Cement Plaster Ceiling	8	Mar-13-24	Mar-22-24
CIC-2410	Cement Plaster Walls	12	Mar-21-24	Apr-05-24
CIC-2420	Fire Protection Piping	10	Mar-25-24	Apr-05-24
CIC-2430	Fire Protection Test	2	Apr-08-24	Apr-09-24
CIC-2440	Topping Installation	5	Apr-08-24	Apr-12-24
CIC-2450	Stair Railings	6	Apr-08-24	Apr-15-24
CIC-2460	Window, Glass & Louver Installation	10	Apr-08-24	Apr-19-24
CIC-2470	Fire Protection Sprinklers	5	Apr-10-24	Apr-16-24
CIC-2480	Shower Base	3	Apr-15-24	Apr-17-24
CIC-2490	Terrace Tile Water Proofing	5	Apr-15-24	Apr-19-24
CIC-2500	GB Installation	10	Apr-15-24	Apr-26-24
CIC-2510	Floor Tile Installation	10	Apr-18-24	May-01-24
CIC-2520	Terrace Railings	5	Apr-25-24	May-01-24
CIC-2530	Sliding Doors Installation	8	Apr-25-24	May-06-24
CIC-2540	Base Tile Waterproofing	5	Apr-29-24	May-03-24
CIC-2550	Ceiling & Wall Primert & 1st Coat	12	Apr-29-24	May-14-24
CIC-2560	Interior Wood Door Installation	12	May-01-24	May-16-24
CIC-2570	Hollow Metal Doors Installation	4	May-02-24	May-07-24
CIC-2580	Entrance Doors Installation	5	May-02-24	May-08-24
CIC-2590	Closet Mirror Doors Installation	8	May-07-24	May-16-24
CIC-2600	Kitchen Installation	8	May-07-24	May-16-24
CIC-2610	Wall Tile Installation	6	May-09-24	May-16-24
CIC-2620	Doors Paint	10	May-09-24	May-22-24
CIC-2630	Intercom System Installation	4	May-15-24	May-20-24
CIC-2640	Wiring Devices	8	May-15-24	May-24-24
CIC-2650	Plumbing Fixtures	8	May-15-24	May-24-24
CIC-2660	Doors Hardware Installation	8	May-16-24	May-27-24
CIC-2670	Apartments Electrical Panel Installation	8	May-16-24	May-27-24
CIC-2680	Ceiling & Wall Paint Finish Coat	10	May-16-24	May-29-24
CIC-2690	Apartments Exhaust Fan Diffuser Installation	8	May-17-24	May-28-24
CIC-2700	Bathroom Accessories	6	May-22-24	May-29-24
CIC-2710	Electrical Rooms Meterbanks Installation	3	May-23-24	May-27-24
CIC-2720	New Appliances	4	May-24-24	May-29-24
CIC-2730	Substantial Completion	0		May-29-24
CIC-2740	Punch List	20	May-30-24	Jun-26-24
6th Floor		176	Jan-03-24	Sep-04-24

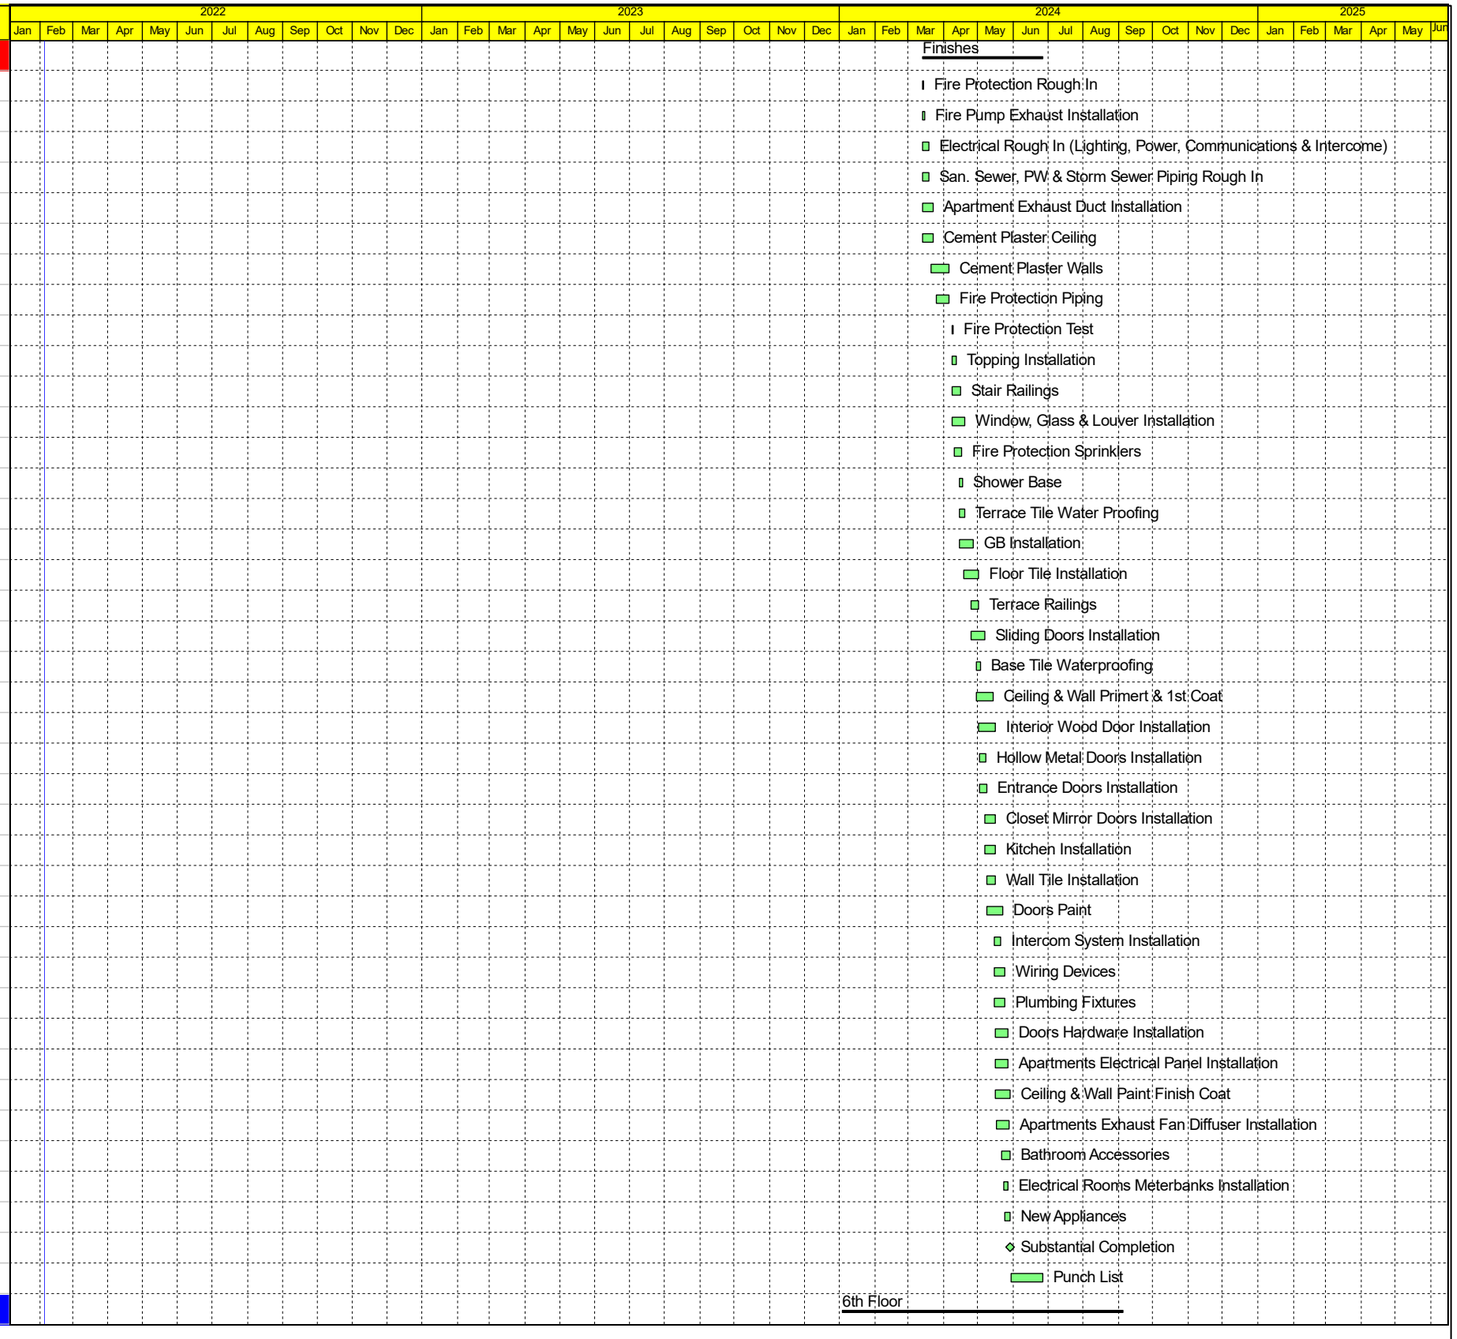

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
Civil/Structural		100	Jan-03-24	May-21-24
CIC-1400	6th Level Concrete Slab	20	Jan-03-24	Jan-30-24
CIC-1405	6th Level Concrete Walls	30	Jan-31-24	Mar-12-24
CIC-1475	CMU Installation 6th Floor	30	Apr-10-24	May-21-24
CIC-2780	Concrete Stairs FRP	10	Apr-17-24	Apr-30-24
Finishes		76	May-22-24	Sep-04-24
CIC-2770	Fire Protection Rough In	2	May-22-24	May-23-24
CIC-2800	Fire Pump Exhaust Installation	3	May-22-24	May-24-24
CIC-2750	Electrical Rough In (Lighting, Power, Communications & Intercome	5	May-22-24	May-28-24
CIC-2760	San. Sewer, PW & Storm Sewer Piping Rough In	5	May-22-24	May-28-24
CIC-2790	Apartment Exhaust Duct Installation	8	May-22-24	May-31-24
CIC-2810	Cement Plaster Ceiling	8	May-22-24	May-31-24
CIC-2820	Cement Plaster Walls	12	May-30-24	Jun-14-24
CIC-2830	Fire Protection Piping	10	Jun-03-24	Jun-14-24
CIC-2840	Fire Protection Test	2	Jun-17-24	Jun-18-24
CIC-2850	Topping Installation	5	Jun-17-24	Jun-21-24
CIC-2860	Stair Railings	6	Jun-17-24	Jun-24-24
CIC-2870	Window, Glass & Louver Installation	10	Jun-17-24	Jun-28-24
CIC-2880	Fire Protection Sprinklers	5	Jun-19-24	Jun-25-24
CIC-2890	Shower Base	3	Jun-24-24	Jun-26-24
CIC-2900	Terrace Tile Water Proofing	5	Jun-24-24	Jun-28-24
CIC-2910	GB Installation	10	Jun-24-24	Jul-05-24
CIC-2920	Floor Tile Installation	10	Jun-27-24	Jul-10-24
CIC-2930	Terrace Railings	5	Jul-04-24	Jul-10-24
CIC-2940	Sliding Doors Installation	8	Jul-04-24	Jul-15-24
CIC-2950	Base Tile Waterproofing	5	Jul-08-24	Jul-12-24
CIC-2960	Ceiling & Wall Primert & 1st Coat	12	Jul-08-24	Jul-23-24
CIC-2970	Interior Wood Door Installation	12	Jul-10-24	Jul-25-24
CIC-2980	Hollow Metal Doors Installation	4	Jul-11-24	Jul-16-24
CIC-2990	Entrance Doors Installation	5	Jul-11-24	Jul-17-24
CIC-3000	Closet Mirror Doors Installation	8	Jul-16-24	Jul-25-24
CIC-3010	Kitchen Installation	8	Jul-16-24	Jul-25-24
CIC-3020	Wall Tile Installation	6	Jul-18-24	Jul-25-24
CIC-3030	Doors Paint	10	Jul-18-24	Jul-31-24
CIC-3040	Intercom System Installation	4	Jul-24-24	Jul-29-24
CIC-3050	Wiring Devices	8	Jul-24-24	Aug-02-24
CIC-3060	Plumbing Fixtures	8	Jul-24-24	Aug-02-24
CIC-3070	Doors Hardware Installation	8	Jul-25-24	Aug-05-24
CIC-3080	Apartments Electrical Panel Installation	8	Jul-25-24	Aug-05-24
CIC-3090	Ceiling & Wall Paint Finish Coat	10	Jul-25-24	Aug-07-24
CIC-3100	Apartments Exhaust Fan Diffuser Installation	8	Jul-26-24	Aug-06-24
CIC-3110	Bathroom Accessories	6	Jul-31-24	Aug-07-24

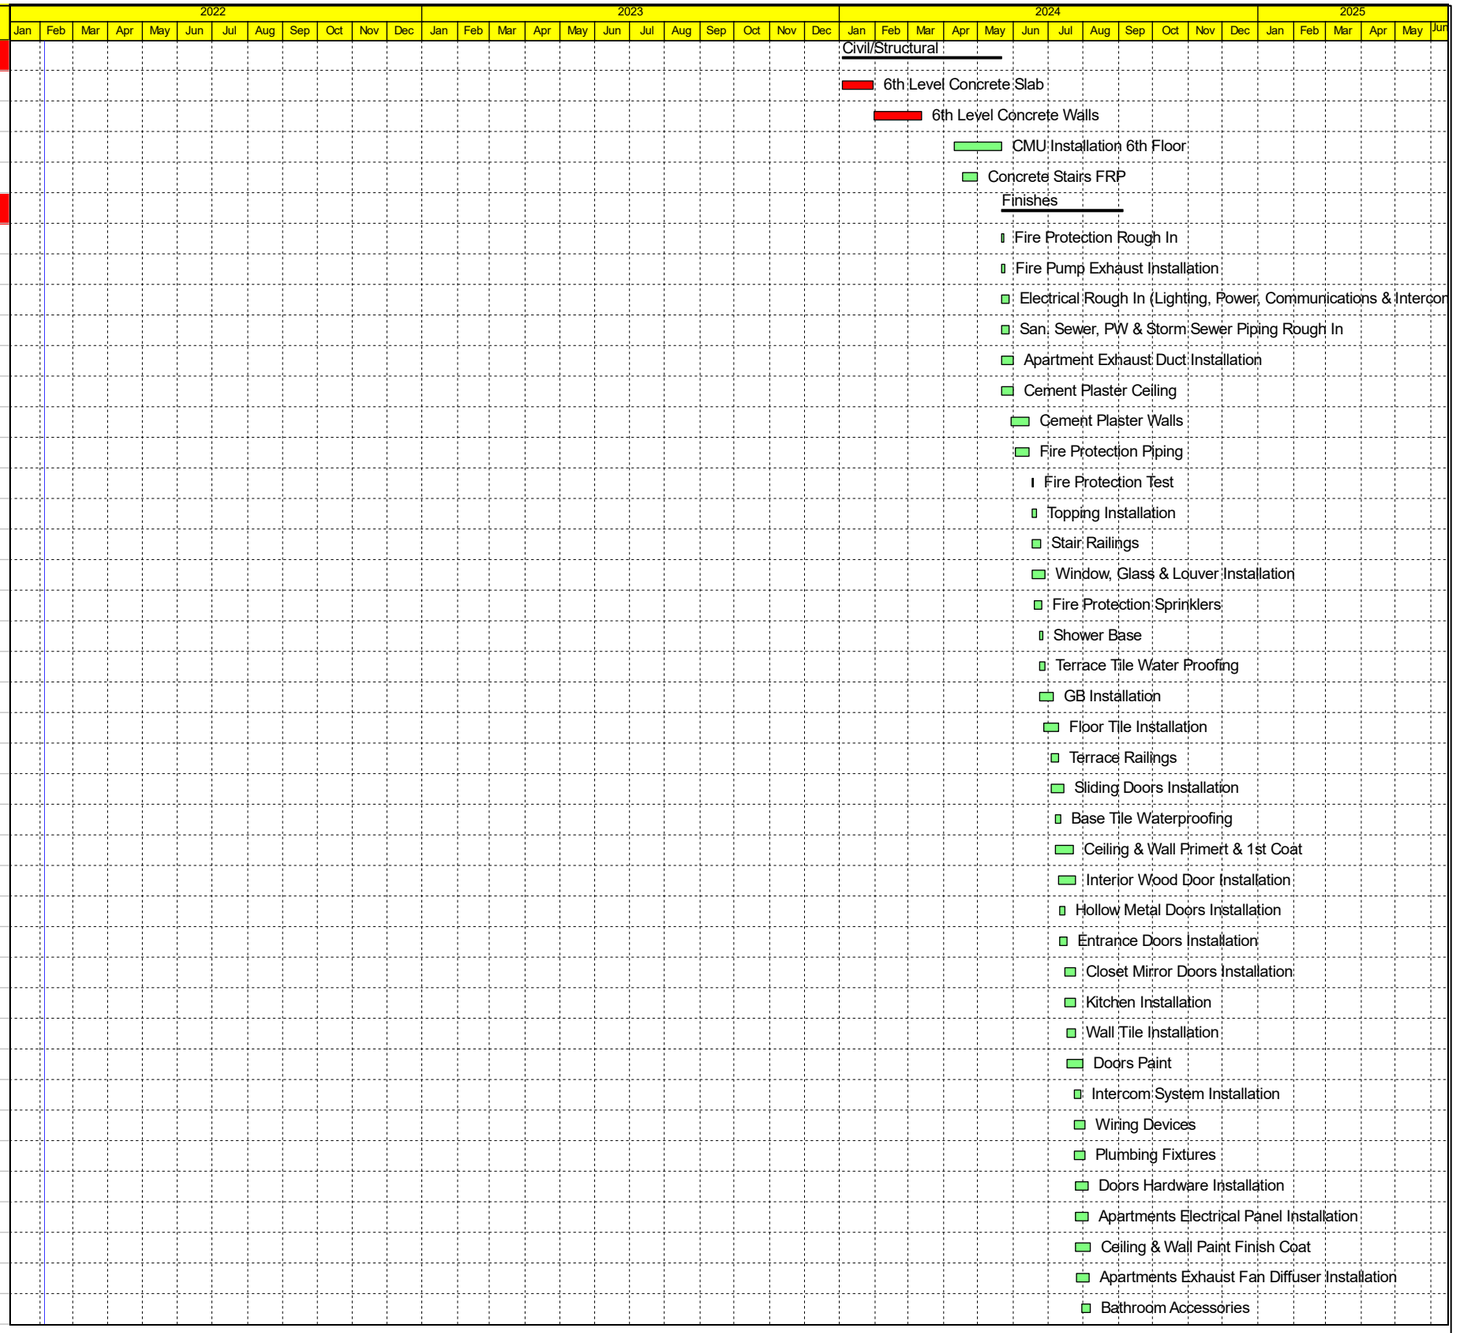


- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.
CIC Construction Group, S.E.
Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-3120	Electrical Rooms Meterbanks Installation	3	Aug-01-24	Aug-05-24
CIC-3130	New Appliances	4	Aug-02-24	Aug-07-24
CIC-3140	Substantial Completion	0		Aug-07-24
CIC-3150	Punch List	20	Aug-08-24	Sep-04-24
7th Floor		161	Mar-13-24	Oct-23-24
Civil/Structural		85	Mar-13-24	Jul-09-24
CIC-1410	7th Level Concrete Slab	20	Mar-13-24	Apr-09-24
CIC-1415	7th Level Concrete Walls	15	Apr-10-24	Apr-30-24
CIC-3190	Concrete Stairs FRP	10	May-29-24	Jun-11-24
CIC-1480	CMU Installation 7th Floor	30	May-29-24	Jul-09-24
Finishes		76	Jul-10-24	Oct-23-24
CIC-3180	Fire Protection Rough In	2	Jul-10-24	Jul-11-24
CIC-3210	Fire Pump Exhaust Installation	3	Jul-10-24	Jul-12-24
CIC-3160	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Jul-10-24	Jul-16-24
CIC-3170	San. Sewer, PW & Storm Sewer Piping Rough In	5	Jul-10-24	Jul-16-24
CIC-3200	Apartment Exhaust Duct Installation	8	Jul-10-24	Jul-19-24
CIC-3220	Cement Plaster Ceiling	8	Jul-10-24	Jul-19-24
CIC-3230	Cement Plaster Walls	12	Jul-18-24	Aug-02-24
CIC-3240	Fire Protection Piping	10	Jul-22-24	Aug-02-24
CIC-3250	Fire Protection Test	2	Aug-05-24	Aug-06-24
CIC-3260	Topping Installation	5	Aug-05-24	Aug-09-24
CIC-3270	Stair Railings	6	Aug-05-24	Aug-12-24
CIC-3280	Window, Glass & Louver Installation	10	Aug-05-24	Aug-16-24
CIC-3290	Fire Protection Sprinklers	5	Aug-07-24	Aug-13-24
CIC-3300	Shower Base	3	Aug-12-24	Aug-14-24
CIC-3310	Terrace Tile Water Proofing	5	Aug-12-24	Aug-16-24
CIC-3320	GB Installation	10	Aug-12-24	Aug-23-24
CIC-3330	Floor Tile Installation	10	Aug-15-24	Aug-28-24
CIC-3340	Terrace Railings	5	Aug-22-24	Aug-28-24
CIC-3350	Sliding Doors Installation	8	Aug-22-24	Sep-02-24
CIC-3360	Base Tile Waterproofing	5	Aug-26-24	Aug-30-24
CIC-3370	Ceiling & Wall Primert & 1st Coat	12	Aug-26-24	Sep-10-24
CIC-3380	Interior Wood Door Installation	12	Aug-28-24	Sep-12-24
CIC-3390	Hollow Metal Doors Installation	4	Aug-29-24	Sep-03-24
CIC-3400	Entrance Doors Installation	5	Aug-29-24	Sep-04-24
CIC-3410	Closet Mirror Doors Installation	8	Sep-03-24	Sep-12-24
CIC-3420	Kitchen Installation	8	Sep-03-24	Sep-12-24
CIC-3430	Wall Tile Installation	6	Sep-05-24	Sep-12-24
CIC-3440	Doors Paint	10	Sep-05-24	Sep-18-24
CIC-3450	Intercom System Installation	4	Sep-11-24	Sep-16-24
CIC-3460	Wiring Devices	8	Sep-11-24	Sep-20-24
CIC-3470	Plumbing Fixtures	8	Sep-11-24	Sep-20-24

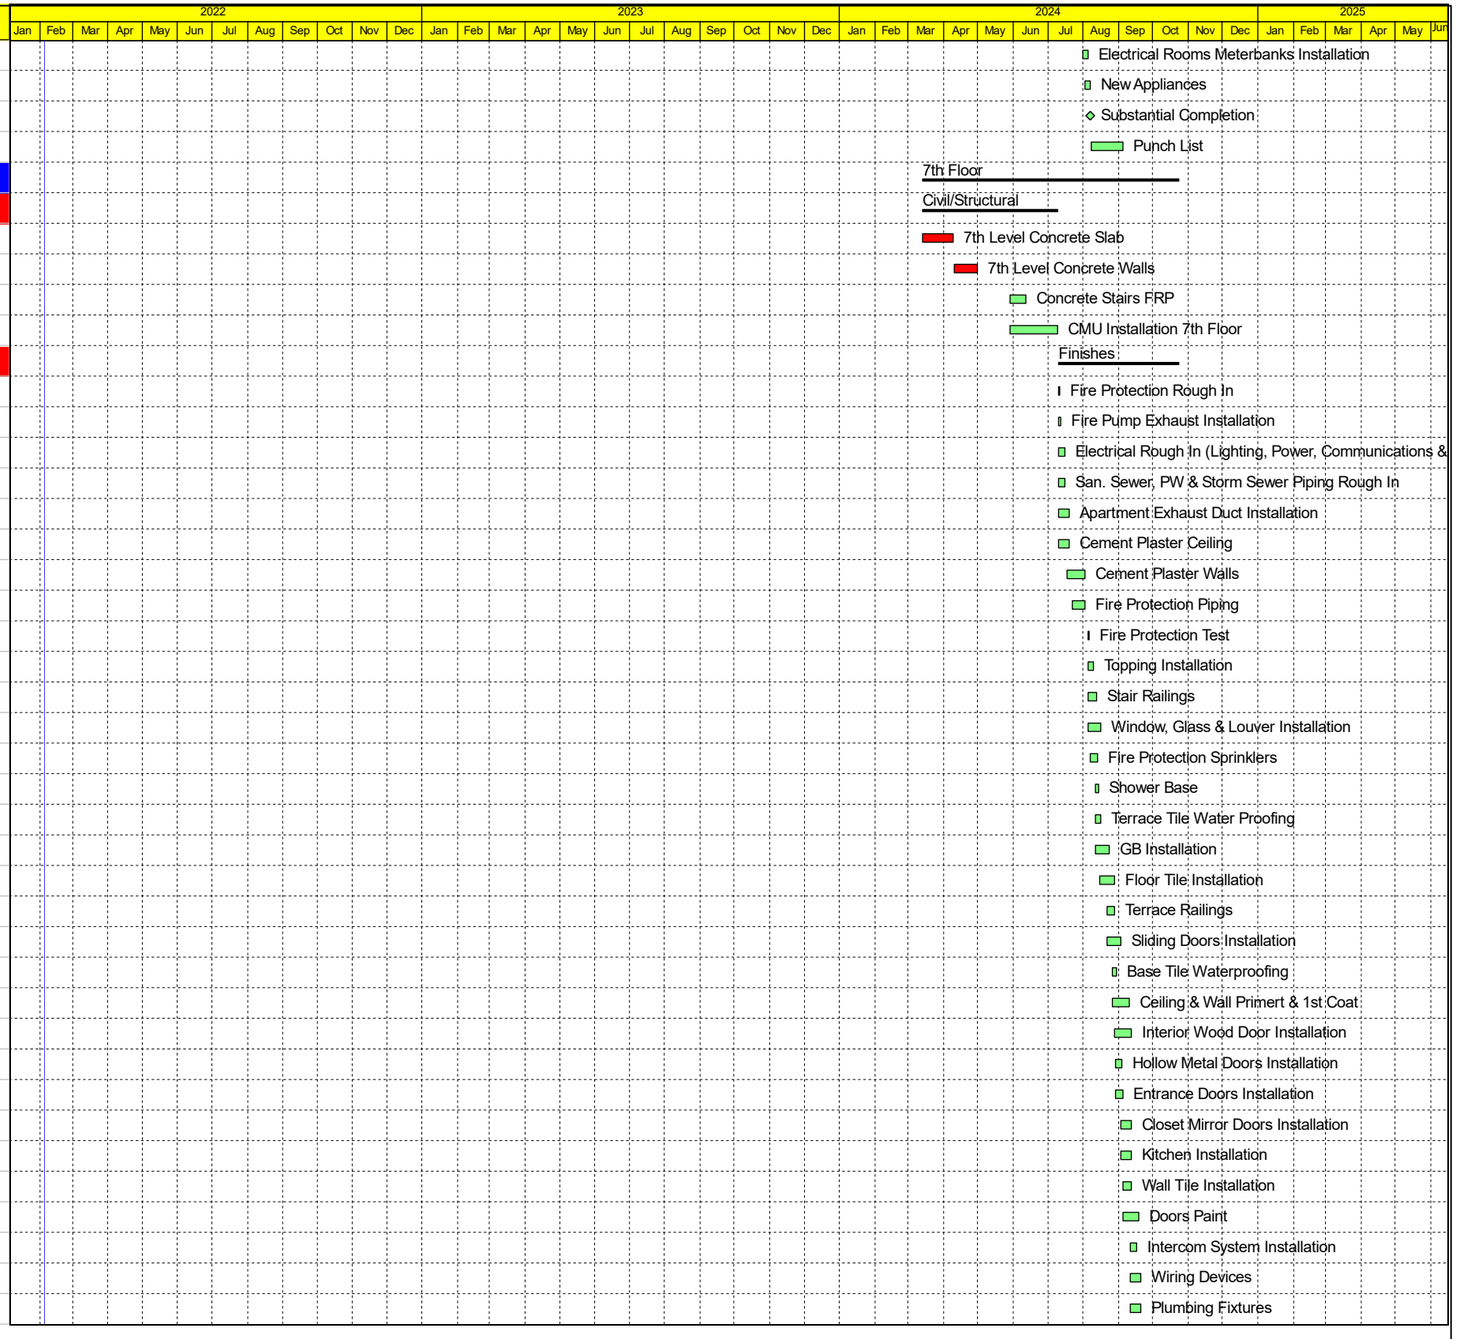

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.


CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-3480	Doors Hardware Installation	8	Sep-12-24	Sep-23-24
CIC-3490	Apartments Electrical Panel Installation	8	Sep-12-24	Sep-23-24
CIC-3500	Ceiling & Wall Paint Finish Coat	10	Sep-12-24	Sep-25-24
CIC-3510	Apartments Exhaust Fan Diffuser Installation	8	Sep-13-24	Sep-24-24
CIC-3520	Bathroom Accessories	6	Sep-18-24	Sep-25-24
CIC-3530	Electrical Rooms Meterbanks Installation	3	Sep-19-24	Sep-23-24
CIC-3540	New Appliances	4	Sep-20-24	Sep-25-24
CIC-3550	Substantial Completion	0		Sep-25-24
CIC-3560	Punch List	20	Sep-26-24	Oct-23-24
8th Floor		167	May-01-24	Dec-19-24
Civil/Structural		91	May-01-24	Sep-04-24
CIC-1430	8th Level Concrete Slab	20	May-01-24	May-28-24
CIC-1435	8th Level Concrete Walls	15	May-29-24	Jun-18-24
CIC-3600	Concrete Stairs FRP	10	Jun-12-24	Jun-25-24
CIC-1490	CMU Installation 8th Floor	30	Jul-25-24	Sep-04-24
Finishes		76	Sep-05-24	Dec-19-24
CIC-3590	Fire Protection Rough In	2	Sep-05-24	Sep-06-24
CIC-3620	Fire Pump Exhaust Installation	3	Sep-05-24	Sep-09-24
CIC-3570	Electrical Rough In (Lighting, Power, Communications & Intercome	5	Sep-05-24	Sep-11-24
CIC-3580	San. Sewer, PW & Storm Sewer Piping Rough In	5	Sep-05-24	Sep-11-24
CIC-3610	Apartment Exhaust Duct Installation	8	Sep-05-24	Sep-16-24
CIC-3630	Cement Plaster Ceiling	8	Sep-05-24	Sep-16-24
CIC-3640	Cement Plaster Walls	12	Sep-13-24	Sep-30-24
CIC-3650	Fire Protection Piping	10	Sep-17-24	Sep-30-24
CIC-3660	Fire Protection Test	2	Oct-01-24	Oct-02-24
CIC-3670	Topping Installation	5	Oct-01-24	Oct-07-24
CIC-3680	Stair Railings	6	Oct-01-24	Oct-08-24
CIC-3690	Window, Glass & Louver Installation	10	Oct-01-24	Oct-14-24
CIC-3700	Fire Protection Sprinklers	5	Oct-03-24	Oct-09-24
CIC-3710	Shower Base	3	Oct-08-24	Oct-10-24
CIC-3720	Terrace Tile Water Proofing	5	Oct-08-24	Oct-14-24
CIC-3730	GB Installation	10	Oct-08-24	Oct-21-24
CIC-3740	Floor Tile Installation	10	Oct-11-24	Oct-24-24
CIC-3750	Terrace Railings	5	Oct-18-24	Oct-24-24
CIC-3760	Sliding Doors Installation	8	Oct-18-24	Oct-29-24
CIC-3770	Base Tile Waterproofing	5	Oct-22-24	Oct-28-24
CIC-3780	Ceiling & Wall Primert & 1st Coat	12	Oct-22-24	Nov-06-24
CIC-3790	Interior Wood Door Installation	12	Oct-24-24	Nov-08-24
CIC-3800	Hollow Metal Doors Installation	4	Oct-25-24	Oct-30-24
CIC-3810	Entrance Doors Installation	5	Oct-25-24	Oct-31-24
CIC-3820	Closet Mirror Doors Installation	8	Oct-30-24	Nov-08-24
CIC-3830	Kitchen Installation	8	Oct-30-24	Nov-08-24

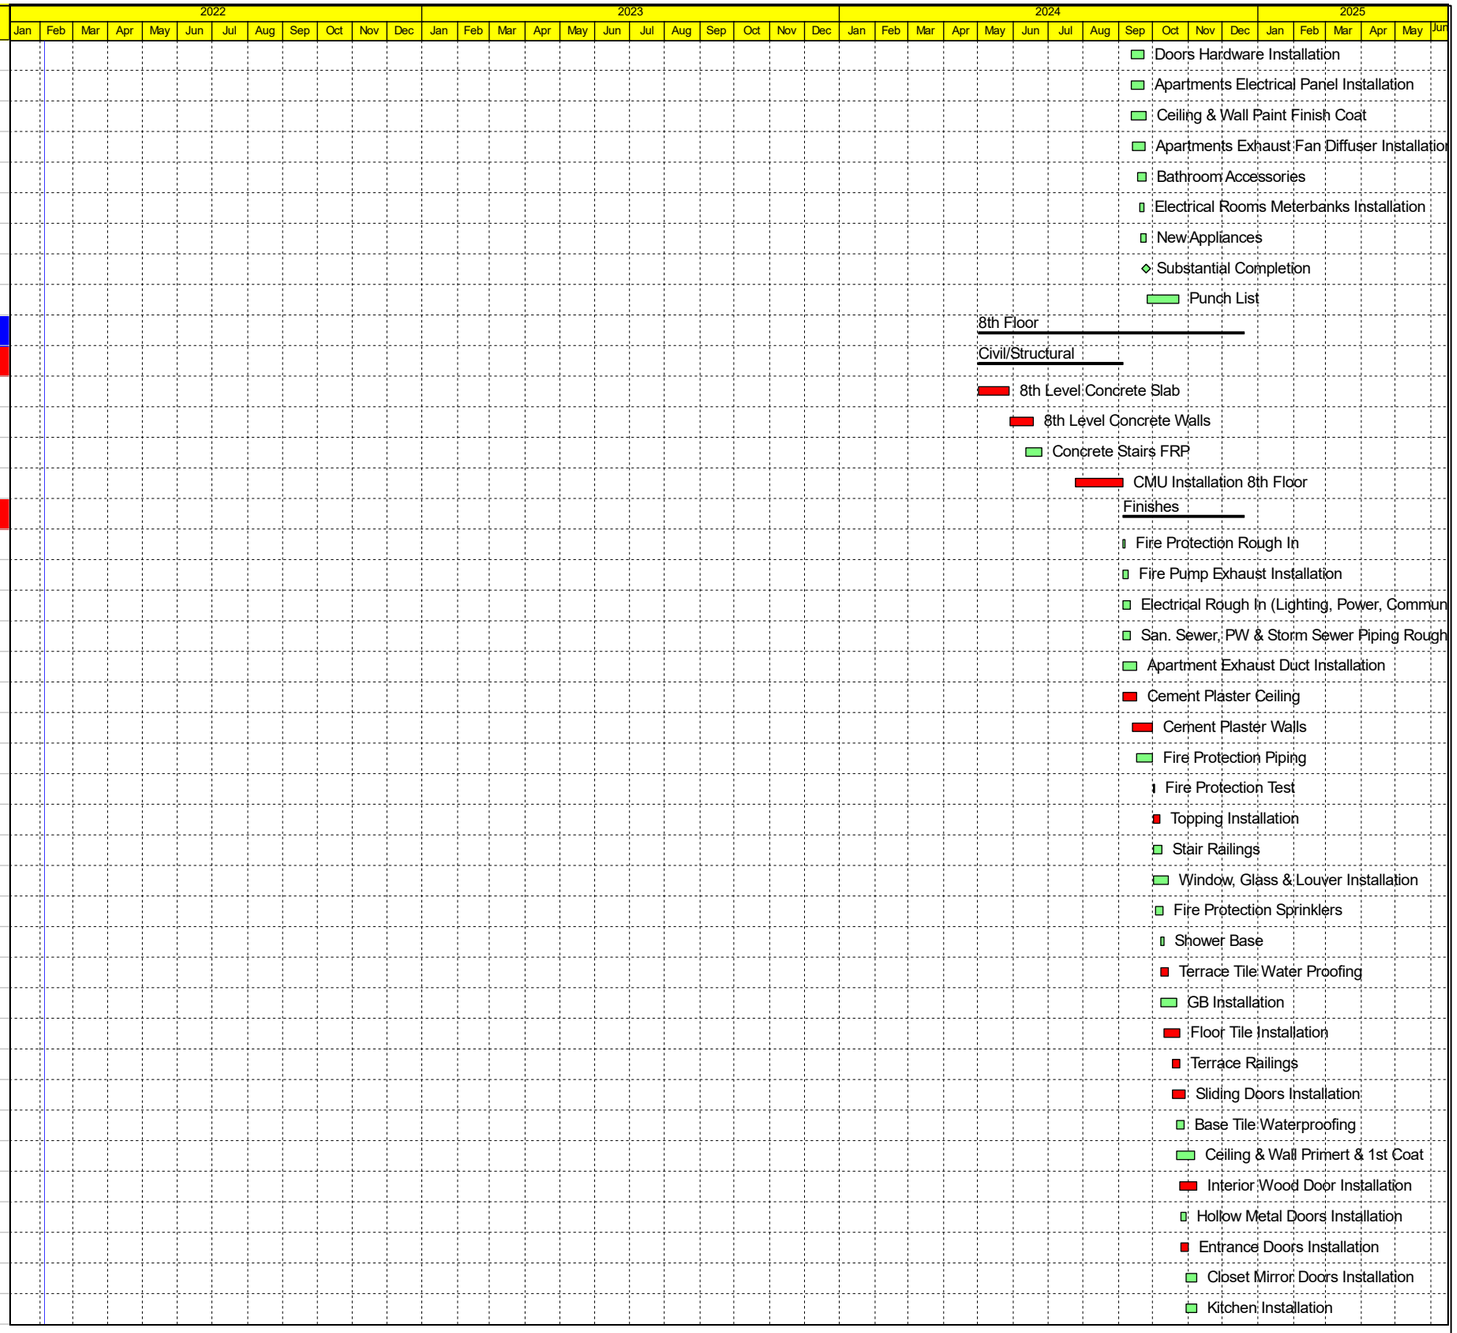

- Project Start: Feb-04-22
- Project Finish: Jan-16-25
- Data Date: Feb-04-22
- Run Date: Feb-04-22
- (c) Oracle- Primavera P6

Egida 387 -Guaynabo, P.R.

CIC Construction Group, S.E.

Quote Schedule

CIC Construction GROUP

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone Critical
Actual Milestone
Summary

Activity ID	Activity Name	Original Duration	Start	Finish
CIC-3840	Wall Tile Installation	6	Nov-01-24	Nov-08-24
CIC-3850	Doors Paint	10	Nov-01-24	Nov-14-24
CIC-3860	Intercom System Installation	4	Nov-07-24	Nov-12-24
CIC-3870	Wiring Devices	8	Nov-07-24	Nov-18-24
CIC-3880	Plumbing Fixtures	8	Nov-07-24	Nov-18-24
CIC-3890	Doors Hardware Installation	8	Nov-08-24	Nov-19-24
CIC-3900	Apartments Electrical Panel Installation	8	Nov-08-24	Nov-19-24
CIC-3910	Ceiling & Wall Paint Finish Coat	10	Nov-08-24	Nov-21-24
CIC-3920	Apartments Exhaust Fan Diffuser Installation	8	Nov-11-24	Nov-20-24
CIC-3930	Bathroom Accessories	6	Nov-14-24	Nov-21-24
CIC-3940	Electrical Rooms Meterbanks Installation	3	Nov-15-24	Nov-19-24
CIC-3950	New Appliances	4	Nov-18-24	Nov-21-24
CIC-3960	Substantial Completion	0		Nov-21-24
CIC-3970	Punch List	20	Nov-22-24	Dec-19-24
Roof Floor		55	Jun-06-24	Aug-21-24
CIC-1550	Roof Forms & Rebar	15	Jun-06-24	Jun-26-24
CIC-1440	Roof Concrete	20	Jun-27-24	Jul-24-24
CIC-1545	Roofing System	20	Jul-25-24	Aug-21-24
Project Completion		36	Nov-27-24	Jan-16-25
CIC-1570	Project Substantial Completion	0		Nov-27-24
CIC-1575	Final Completion & Demobilization	20	Dec-20-24	Jan-16-25

